


Stavební úpravy Terminálu 3

ID	Režim úkolu	Název úkolu	Doba trvání	Zahájení	Dokončení	Kalendářní plán (Gantt chart)																																											
						VII 2021			VIII 2021			IX 2021			X 2021			XI 2021			XII 2021			I 2022			II 2022			III 2022			IV 2022			V 2022													
						21.	28.	05.	12.	19.	26.	02.	09.	16.	23.	30.	06.	13.	20.	27.	04.	11.	18.	25.	01.	08.	15.	22.	29.	06.	13.	20.	27.	03.	10.	17.	24.	31.	07.	14.	21.	28.	04.	11.	18.	25.	02.	09.	16.
1	➡	Příprava projektu	32 dny	30.06. 21	01.08. 21	[Bar chart: 30.06. to 01.08. 21]																																											
2	➡	Oznámení o vítězství v soutěži	0 dny	30.06. 21	30.06. 21	[Bar chart: 30.06. 21]																																											
3	➡	VŘ na subdodavatele Bourací práce, OK, vstupy, EL, RTCH, SDK, střechy	31 dny	02.07. 21	01.08. 21	[Bar chart: 02.07. 21 to 01.08. 21]																																											
4	➡	Stavební úpravy Terminálu 3	306 dny	01.07. 21	02.05. 22	[Large bar chart: 01.07. 21 to 02.05. 22]																																											
5	➡	Předání staveniště	1 den	02.08. 21	02.08. 21	[Bar chart: 02.08. 21]																																											
6	➡	I. fáze realizace	78 dny	01.07. 21	16.09. 21	[Bar chart: 01.07. 21 to 16.09. 21]																																											
7	➡	Realizace stavebních záborů	14 dny	03.08. 21	16.08. 21	[Bar chart: 03.08. 21 to 16.08. 21]																																											
8	➡	Výkop základů pro vstup "A" a podkladní beton	14 dny	03.08. 21	16.08. 21	[Bar chart: 03.08. 21 to 16.08. 21]																																											
9	➡	Dílenská dokumentace vstupu "A"	14 dny	03.08. 21	16.08. 21	[Bar chart: 03.08. 21 to 16.08. 21]																																											
10	➡	Dílenská dokumentace provizorní pasové přepážky stanoviště BEK	14 dny	03.08. 21	16.08. 21	[Bar chart: 03.08. 21 to 16.08. 21]																																											
11	➡	Milník č.1	0 dny	16.08. 21	16.08. 21	[Milestone: 16.08. 21]																																											
12	➡	SO 04 - Provizorní stav	78 dny	01.07. 21	16.09. 21	[Bar chart: 01.07. 21 to 16.09. 21]																																											
13	➡	Dočasné stanoviště BEK	21 dny	17.08. 21	06.09. 21	[Bar chart: 17.08. 21 to 06.09. 21]																																											
14	➡	Dočasná přepážka pasové kontroly	10 dny	07.09. 21	16.09. 21	[Bar chart: 07.09. 21 to 16.09. 21]																																											
15	➡	Komunikační koridor	21 dny	17.08. 21	06.09. 21	[Bar chart: 17.08. 21 to 06.09. 21]																																											
16	➡	Silnoproudé rozvody SO 04	14 dny	31.08. 21	13.09. 21	[Bar chart: 31.08. 21 to 13.09. 21]																																											
17	➡	SLB rozvody SO 04	14 dny	01.07. 21	14.07. 21	[Bar chart: 01.07. 21 to 14.07. 21]																																											
18	➡	Komplexní zkouška požárních systémů	1 den	14.09. 21	14.09. 21	[Bar chart: 14.09. 21]																																											
19	➡	Předčasné užívání Díla SO 04	0 dny	16.09. 21	16.09. 21	[Milestone: 16.09. 21]																																											
20	➡	Základy pro vstup "A"	21 dny	17.08. 21	06.09. 21	[Bar chart: 17.08. 21 to 06.09. 21]																																											
21	➡	Výkop základů pro OK airside	24 dny	24.08. 21	16.09. 21	[Bar chart: 24.08. 21 to 16.09. 21]																																											
22	➡	Výrobně-dílenská dokumentace OK zastřešení v airside	45 dny	01.07. 21	14.08. 21	[Bar chart: 01.07. 21 to 14.08. 21]																																											
23	➡	Milník č.2	0 dny	16.09. 21	16.09. 21	[Milestone: 16.09. 21]																																											
24	➡	II. fáze realizace	259 dny	17.08. 21	02.05. 22	[Bar chart: 17.08. 21 to 02.05. 22]																																											
25	➡	Realizace nového vstupu "A"	28 dny	07.09. 21	04.10. 21	[Bar chart: 07.09. 21 to 04.10. 21]																																											
26	➡	Přípojka SIL a SLB pro posuvné dveře	7 dny	05.10. 21	11.10. 21	[Bar chart: 05.10. 21 to 11.10. 21]																																											
27	➡	Komplexní zkouška vstup "A" dle PBŘS	1 den	12.10. 21	12.10. 21	[Bar chart: 12.10. 21]																																											
28	➡	Bourací práce II.fáze díla	28 dny	17.09. 21	14.10. 21	[Bar chart: 17.09. 21 to 14.10. 21]																																											
29	➡	Vyzdívky	28 dny	27.09. 21	24.10. 21	[Bar chart: 27.09. 21 to 24.10. 21]																																											
30	➡	Omítky	30 dny	25.10. 21	23.11. 21	[Bar chart: 25.10. 21 to 23.11. 21]																																											
31	➡	SDK konstrukce	70 dny	09.11. 21	17.01. 22	[Bar chart: 09.11. 21 to 17.01. 22]																																											
32	➡	Kabelové trasy	80 dny	10.10. 21	28.12. 21	[Bar chart: 10.10. 21 to 28.12. 21]																																											
33	➡	Rozvody VZT	80 dny	10.10. 21	28.12. 21	[Bar chart: 10.10. 21 to 28.12. 21]																																											
34	➡	Rozvody RTCH	80 dny	10.10. 21	28.12. 21	[Bar chart: 10.10. 21 to 28.12. 21]																																											
35	➡	Zámečnické kce přiček, zádveří a stěn	25 dny	26.12. 21	19.01. 22	[Bar chart: 26.12. 21 to 19.01. 22]																																											
36	➡	Prosklené ALU kce	30 dny	25.10. 21	23.11. 21	[Bar chart: 25.10. 21 to 23.11. 21]																																											
37	➡	Příprava podkladu pro dlažby	25 dny	31.12. 21	24.01. 22	[Bar chart: 31.12. 21 to 24.01. 22]																																											
38	➡	Obklady keramické	50 dny	27.12. 21	14.02. 22	[Bar chart: 27.12. 21 to 14.02. 22]																																											
39	➡	Dlažby	40 dny	08.02. 22	19.03. 22	[Bar chart: 08.02. 22 to 19.03. 22]																																											
40	➡	Podhledy	75 dny	10.01. 22	25.03. 22	[Bar chart: 10.01. 22 to 25.03. 22]																																											
41	➡	Malby	90 dny	05.01. 22	04.04. 22	[Bar chart: 05.01. 22 to 04.04. 22]																																											
42	➡	Realizace přepoje UT a TUV v kotelně pro Hotel Ramada	30 dny	20.09. 21	19.10. 21	[Bar chart: 20.09. 21 to 19.10. 21]																																											
43	➡	Realizace rozveden ve 2.NP - mč.238, 238a	15 dny	17.09. 21	01.10. 21	[Bar chart: 17.09. 21 to 01.10. 21]																																											
44	➡	Nové kabelové trasy SLB	28 dny	17.09. 21	14.10. 21	[Bar chart: 17.09. 21 to 14.10. 21]																																											
45	➡	Vybavení a zprovoznění rozveden ve 2.NP - mč.238, 238a	8 dny	15.10. 21	22.10. 21	[Bar chart: 15.10. 21 to 22.10. 21]																																											
46	➡	Realizace mikropilot pro OK zastřešení airside	30 dny	17.09. 21	16.10. 21	[Bar chart: 17.09. 21 to 16.10. 21]																																											
47	➡	Realizace základových patek pro zastřešení airside	30 dny	22.09. 21	21.10. 21	[Bar chart: 22.09. 21 to 21.10. 21]																																											
48	➡	Milník č.3	0 dny	22.10. 21	22.10. 21	[Milestone: 22.10. 21]																																											
49	➡	Střešní plášť	138 dny	17.08. 21	01.01. 22	[Bar chart: 17.08. 21 to 01.01. 22]																																											
50	➡	Demontáž stávající krytiny	70 dny	17.08. 21	25.10. 21	[Bar chart: 17.08. 21 to 25.10. 21]																																											
51	➡	Betonáž stávajících prostupů	60 dny	27.08. 21	25.10. 21	[Bar chart: 27.08. 21 to 25.10. 21]																																											
52	➡	Parozábrana	80 dny	03.09. 21	21.11. 21	[Bar chart: 03.09. 21 to 21.11. 21]																																											

Stavební úpravy Terminálu 3

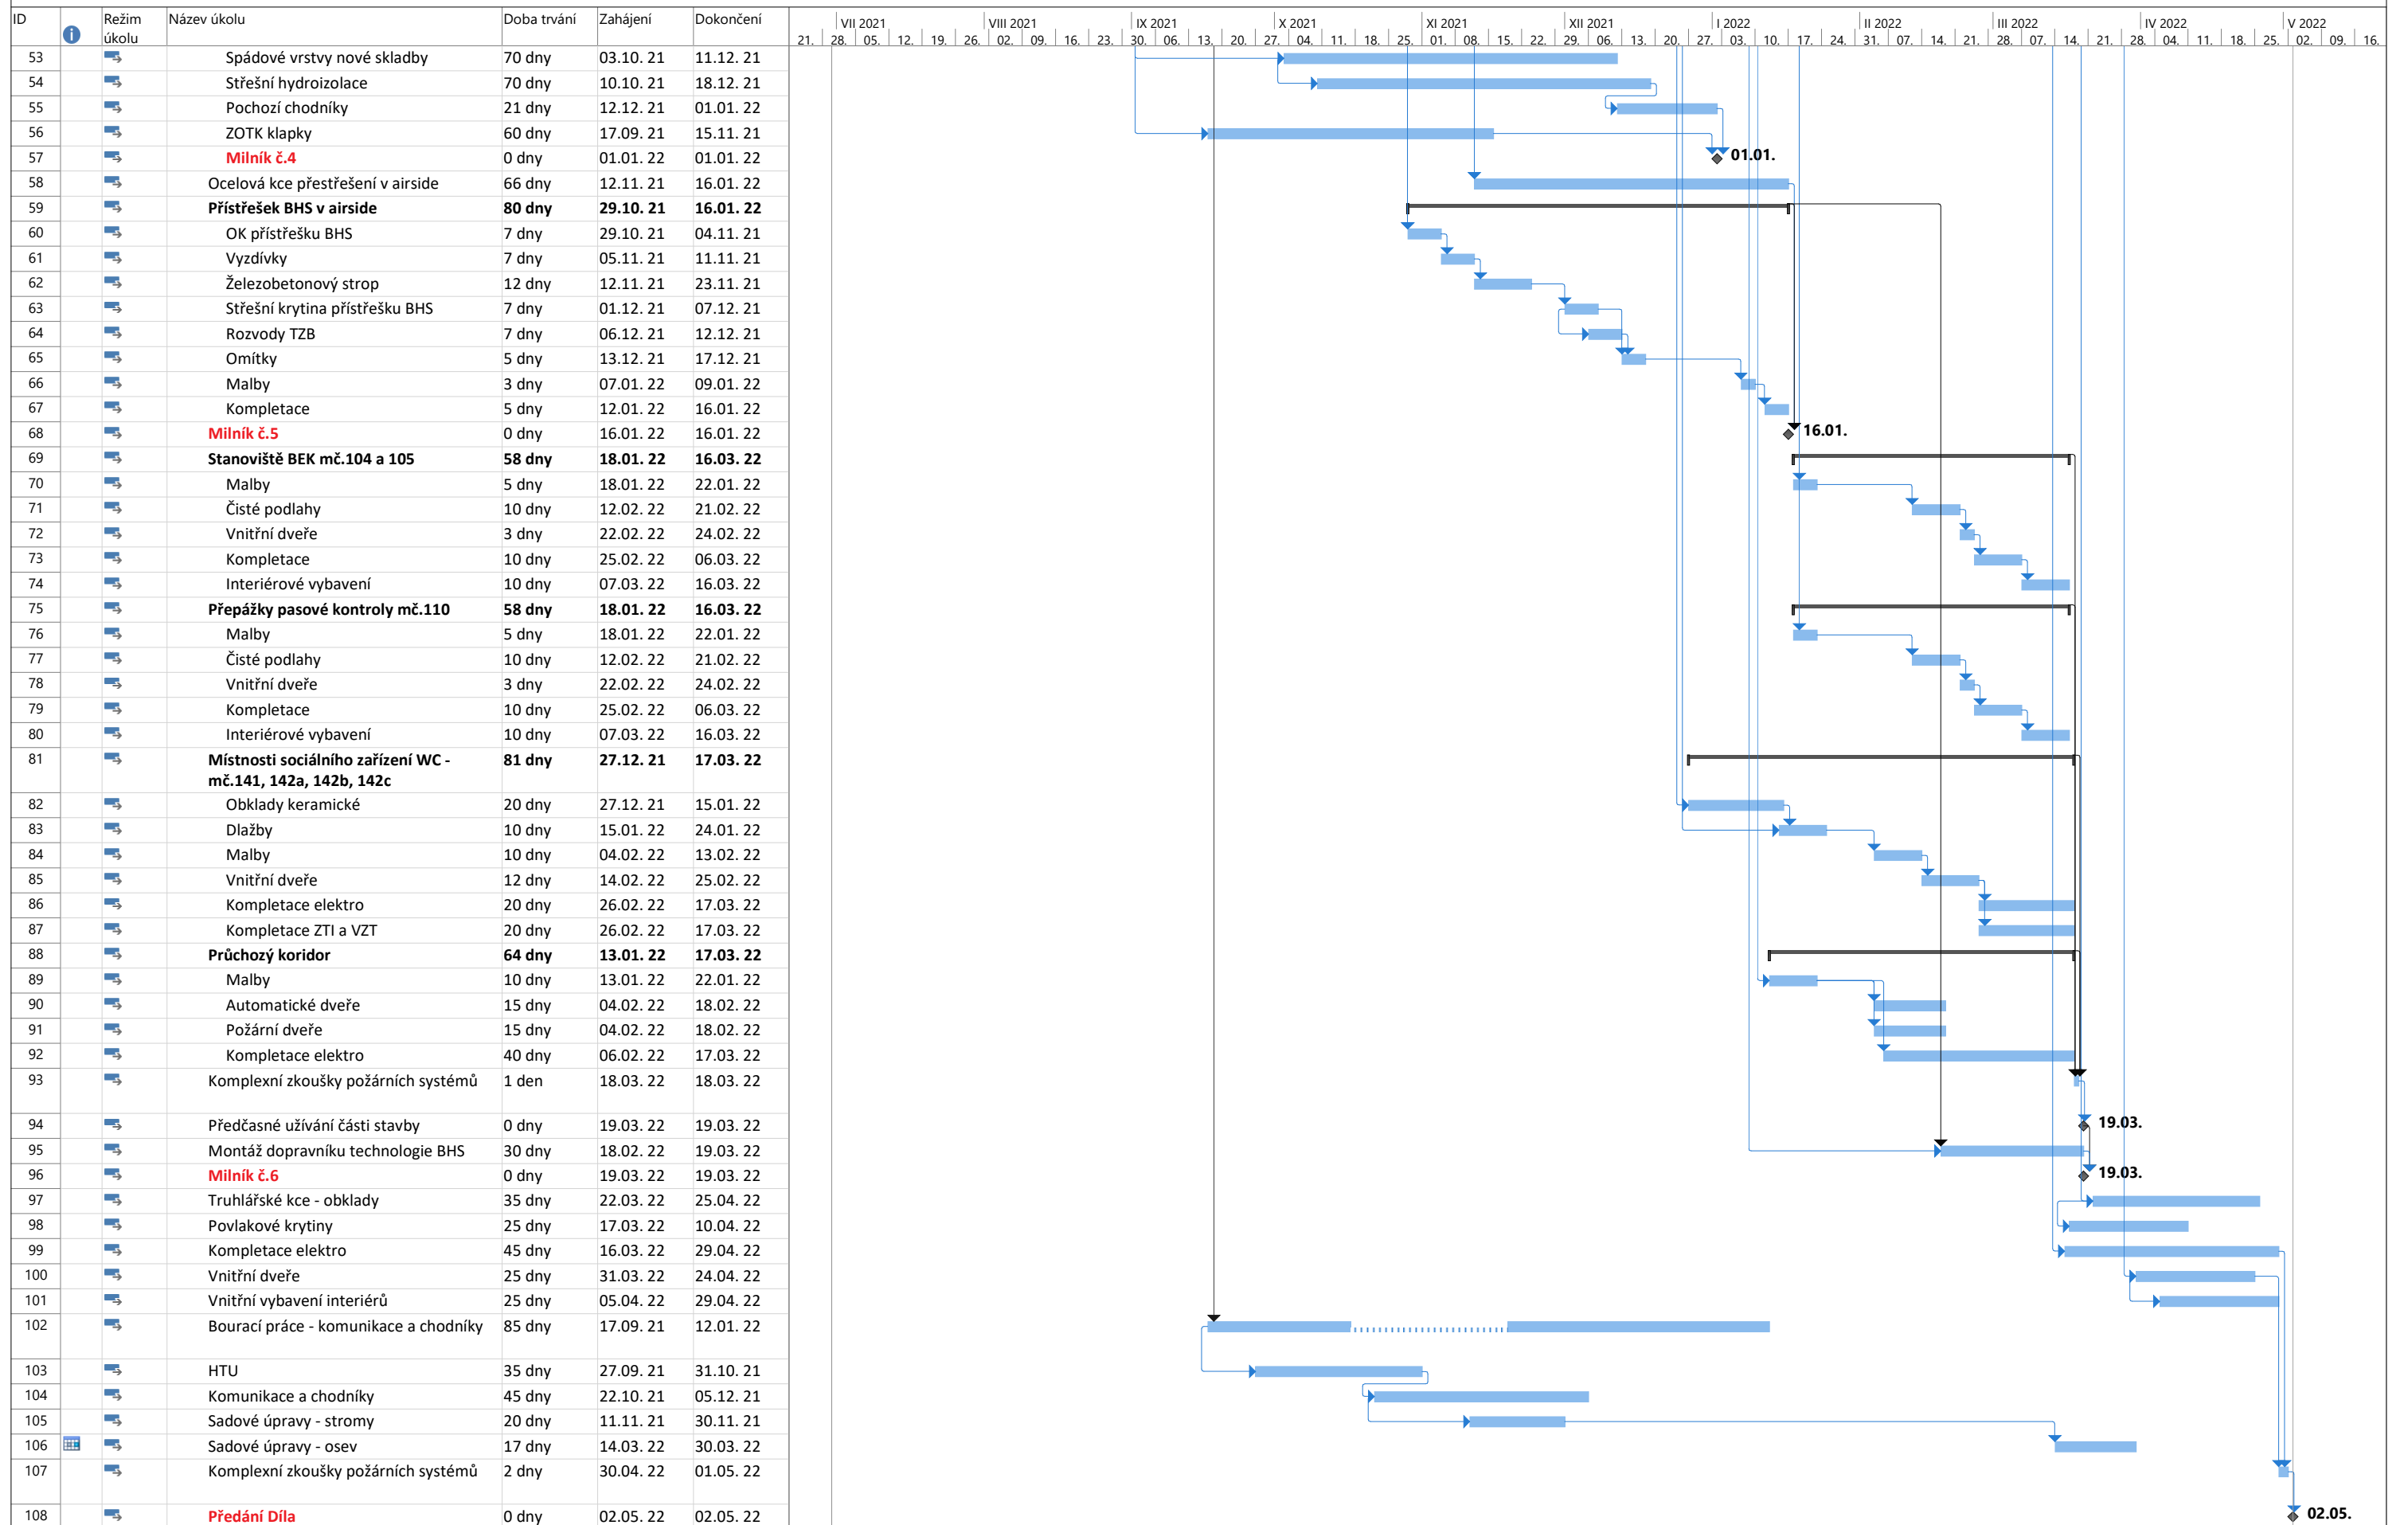

Stavební úpravy Terminálu 3

VI 2022			VII 2022			VIII 2022			IX 2022			X 2022			XI 2022			XII 2022			I 2023			II 2023			III 2023			IV 2023			V 2023			VI 2023			VII 2023			VIII 2023			IX 2023																									
16.	23.	30.	06.	13.	20.	27.	04.	11.	18.	25.	01.	08.	15.	22.	29.	05.	12.	19.	26.	03.	10.	17.	24.	31.	07.	14.	21.	28.	05.	12.	19.	26.	02.	09.	16.	23.	30.	06.	13.	20.	27.	06.	13.	20.	27.	03.	10.	17.	24.	01.	08.	15.	22.	29.	05.	12.	19.	26.	03.	10.	17.	24.	31.	07.	14.	21.	28.	04.	11.	18.

Stavební úpravy Terminálu 3

16.	23.	30.	06.	13.	20.	27.	04.	11.	18.	25.	01.	08.	15.	22.	29.	05.	12.	19.	26.	03.	10.	17.	24.	31.	07.	14.	21.	28.	05.	12.	19.	26.	02.	09.	16.	23.	30.	06.	13.	20.	27.	06.	13.	20.	27.	03.	10.	17.	24.	01.	08.	15.	22.	29.	05.	12.	19.	26.	03.	10.	17.	24.	31.	07.	14.	21.	28.	04.	11.	18.
-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----
