


ID	Descrip	Task Name	Duration	Start	Finish	2026				Half 2, 2026				Half 1, 2027				Half 2, 2027							
						M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O
1		Contract Signature	0 days	06 Apr '26	06 Apr '26																				
2	P1	Payment (20%)	0 wks	06 Apr '26	06 Apr '26																				
3		Project team mobilization	2 wks	06 Apr '26	20 Apr '26																				
4	KOM	Kick-off Meeting	1 day	20 Apr '26	21 Apr '26																				
5		Design and Procedures	12 wks	21 Apr '26	14 Jul '26																				
6	DR	Design Report - M1	0 days	14 Jul '26	14 Jul '26																				
7		Design Report Review and Approval	2 wks	14 Jul '26	28 Jul '26																				
8	P2	Payment (20%)	0 wks	28 Jul '26	28 Jul '26																				
9		Procurement	20 wks	28 Jul '26	15 Dec '26																				
10		Manufacturing	16 wks	15 Dec '26	06 Apr '27																				
11		Factory Testing	8 wks	06 Apr '27	01 Jun '27																				
12	DEL	Report on Factory Acceptance Tests - M2	0 days	01 Jun '27	01 Jun '27																				
13		Packing and Transport to Prague	2 wks	01 Jun '27	15 Jun '27																				
14		Installation and Assembly (supervision Jema)	8 wks	15 Jun '27	10 Aug '27																				
15	ASB	Installation & Assembly - M3	0 wks	10 Aug '27	10 Aug '27																				
16		Commissioning, training and SAT	8 wks	10 Aug '27	05 Oct '27																				
17	SAT	SAT completion	0 days	05 Oct '27	05 Oct '27																				
18	P3	Payment (60%)	0 days	05 Oct '27	05 Oct '27																				

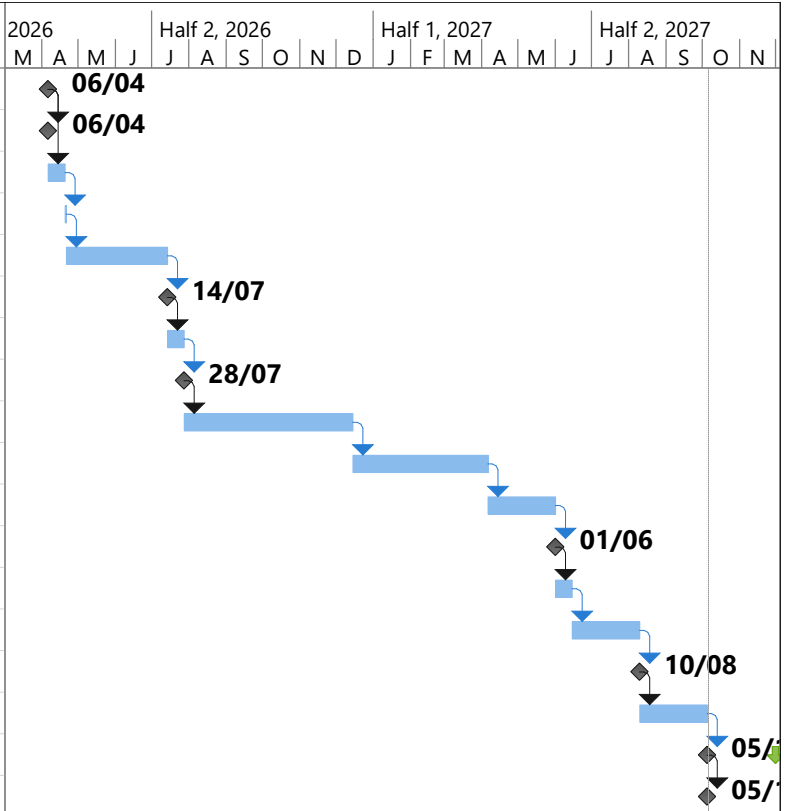

Project: 24-05833 COMPASS Gy
Date: 02 Feb '26

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
