



EUROPEAN CLIMATE, INFRASTRUCTURE AND ENVIRONMENT EXECUTIVE AGENCY (CINEA)

CINEA.B – Sustainable networks and investments
Head of Department

GRANT AGREEMENT

Project 101192431 — 2024-6-CZ-Dormitory

PREAMBLE

This **Agreement** ('the Agreement') is **between** the following parties:

on the one part,

the **European Climate, Infrastructure and Environment Executive Agency (CINEA)** ('EU executive agency' or 'granting authority'), under the powers delegated by the European Commission ('European Commission'),

and

on the other part,

1. 'the coordinator':

OSTRAVSKA UNIVERZITA (OU), PIC 998738870, established in DVORAKOVA 7, OSTRAVA 701 03, Czechia,

Unless otherwise specified, references to 'beneficiary' or 'beneficiaries' include the coordinator and affiliated entities (if any).

If only one beneficiary signs the grant agreement ('mono-beneficiary grant'), all provisions referring to the 'coordinator' or the 'beneficiaries' will be considered — mutatis mutandis — as referring to the beneficiary.

The parties referred to above have agreed to enter into the Agreement.

By signing the Agreement and the accession forms, the beneficiaries accept the grant and agree to implement the action under their own responsibility and in accordance with the Agreement, with all the obligations and terms and conditions it sets out.

The Agreement is composed of:

Preamble

Terms and Conditions (including Data Sheet)

Annex 1	Description of the action ¹
Annex 2	Estimated budget for the action
Annex 3	Accession forms (if applicable) ²
Annex 3a	Declaration on joint and several liability of affiliated entities (if applicable) ³
Annex 4	Model for the financial statements
Annex 5	Specific rules (if applicable)

¹ Template published on [Portal Reference Documents](#).

² Template published on [Portal Reference Documents](#).

³ Template published on [Portal Reference Documents](#).

TERMS AND CONDITIONS

TABLE OF CONTENTS

GRANT AGREEMENT..... 1

PREAMBLE.....1

TERMS AND CONDITIONS.....3

DATASHEET..... 8

CHAPTER 1 GENERAL.....12

ARTICLE 1 — SUBJECT OF THE AGREEMENT 12

ARTICLE 2 — DEFINITIONS..... 12

CHAPTER 2 ACTION..... 13

ARTICLE 3 — ACTION..... 13

ARTICLE 4 — DURATION AND STARTING DATE..... 13

CHAPTER 3 GRANT..... 13

ARTICLE 5 — GRANT..... 13

5.1 Form of grant..... 14

5.2 Maximum grant amount..... 14

5.3 Funding rate..... 14

5.4 Estimated budget, budget categories and forms of funding..... 14

5.5 Budget flexibility..... 14

ARTICLE 6 — ELIGIBLE AND INELIGIBLE CONTRIBUTIONS..... 14

6.1 and 6.2 General and specific eligibility conditions..... 14

6.3 Ineligible contributions..... 15

6.4 Consequences of non-compliance..... 15

CHAPTER 4 GRANT IMPLEMENTATION..... 15

SECTION 1 CONSORTIUM: BENEFICIARIES, AFFILIATED ENTITIES AND OTHER PARTICIPANTS..... 15

ARTICLE 7 — BENEFICIARIES..... 15

ARTICLE 8 — AFFILIATED ENTITIES..... 17

ARTICLE 9 — OTHER PARTICIPANTS INVOLVED IN THE ACTION..... 17

9.1 Associated partners..... 17

9.2 Third parties giving in-kind contributions to the action..... 17

9.3 Subcontractors..... 18

9.4 Recipients of financial support to third parties..... 18

ARTICLE 10 — PARTICIPANTS WITH SPECIAL STATUS.....	18
10.1 Non-EU participants.....	18
10.2 Participants which are international organisations.....	19
10.3 Pillar-assessed participants.....	19
SECTION 2 RULES FOR CARRYING OUT THE ACTION.....	21
ARTICLE 11 — PROPER IMPLEMENTATION OF THE ACTION.....	21
11.1 Obligation to properly implement the action.....	21
11.2 Consequences of non-compliance.....	21
ARTICLE 12 — CONFLICT OF INTERESTS.....	21
12.1 Conflict of interests.....	21
12.2 Consequences of non-compliance.....	22
ARTICLE 13 — CONFIDENTIALITY AND SECURITY.....	22
13.1 Sensitive information.....	22
13.2 Classified information.....	22
13.3 Consequences of non-compliance.....	23
ARTICLE 14 — ETHICS AND VALUES.....	23
14.1 Ethics.....	23
14.2 Values.....	23
14.3 Consequences of non-compliance.....	23
ARTICLE 15 — DATA PROTECTION.....	23
15.1 Data processing by the granting authority.....	23
15.2 Data processing by the beneficiaries.....	24
15.3 Consequences of non-compliance.....	24
ARTICLE 16 — INTELLECTUAL PROPERTY RIGHTS (IPR) — BACKGROUND AND RESULTS — ACCESS RIGHTS AND RIGHTS OF USE.....	24
16.1 Background and access rights to background.....	25
16.2 Ownership of results.....	25
16.3 Rights of use of the granting authority on materials, documents and information received for policy, information, communication, dissemination and publicity purposes.....	25
16.4 Specific rules on IPR, results and background.....	26
16.5 Consequences of non-compliance.....	26
ARTICLE 17 — COMMUNICATION, DISSEMINATION AND VISIBILITY.....	26
17.1 Communication — Dissemination — Promoting the action.....	26
17.2 Visibility — European flag and funding statement.....	26
17.3 Quality of information — Disclaimer.....	27
17.4 Specific communication, dissemination and visibility rules.....	27

17.5	Consequences of non-compliance.....	28
ARTICLE 18 — SPECIFIC RULES FOR CARRYING OUT THE ACTION.....		28
18.1	Specific rules for carrying out the action.....	28
18.2	Consequences of non-compliance.....	28
SECTION 3 GRANT ADMINISTRATION.....		28
ARTICLE 19 — GENERAL INFORMATION OBLIGATIONS.....		28
19.1	Information requests.....	28
19.2	Participant Register data updates.....	28
19.3	Information about events and circumstances which impact the action.....	28
19.4	Consequences of non-compliance.....	29
ARTICLE 20 — RECORD-KEEPING.....		29
20.1	Keeping records and supporting documents.....	29
20.2	Consequences of non-compliance.....	29
ARTICLE 21 — REPORTING.....		29
21.1	Continuous reporting.....	29
21.2	Periodic reporting: Technical reports and financial statements.....	30
21.3	Currency for financial statements and conversion into euros.....	31
21.4	Reporting language.....	31
21.5	Consequences of non-compliance.....	31
ARTICLE 22 — PAYMENTS AND RECOVERIES — CALCULATION OF AMOUNTS DUE.....		31
22.1	Payments and payment arrangements.....	31
22.2	Recoveries.....	31
22.3	Amounts due.....	32
22.4	Enforced recovery.....	36
22.5	Consequences of non-compliance.....	37
ARTICLE 23 — GUARANTEES.....		38
23.1	Prefinancing guarantee.....	38
23.2	Consequences of non-compliance.....	38
ARTICLE 24 — CERTIFICATES.....		38
ARTICLE 25 — CHECKS, REVIEWS, AUDITS AND INVESTIGATIONS — EXTENSION OF FINDINGS.....		38
25.1	Granting authority checks, reviews and audits.....	38
25.2	European Commission checks, reviews and audits in grants of other granting authorities.....	40
25.3	Access to records for assessing simplified forms of funding.....	40
25.4	OLAF, EPPO and ECA audits and investigations.....	40

25.5	Consequences of checks, reviews, audits and investigations — Extension of findings.....	41
25.6	Consequences of non-compliance.....	42
ARTICLE 26 — IMPACT EVALUATIONS.....		42
26.1	Impact evaluation.....	42
26.2	Consequences of non-compliance.....	42
CHAPTER 5 CONSEQUENCES OF NON-COMPLIANCE.....		42
SECTION 1 REJECTIONS AND GRANT REDUCTION.....		42
ARTICLE 27 — REJECTION OF CONTRIBUTIONS.....		42
27.1	Conditions.....	42
27.2	Procedure.....	43
27.3	Effects.....	43
ARTICLE 28 — GRANT REDUCTION.....		43
28.1	Conditions.....	43
28.2	Procedure.....	44
28.3	Effects.....	44
SECTION 2 SUSPENSION AND TERMINATION.....		44
ARTICLE 29 — PAYMENT DEADLINE SUSPENSION.....		44
29.1	Conditions.....	44
29.2	Procedure.....	44
ARTICLE 30 — PAYMENT SUSPENSION.....		45
30.1	Conditions.....	45
30.2	Procedure.....	45
ARTICLE 31 — GRANT AGREEMENT SUSPENSION.....		46
31.1	Consortium-requested GA suspension.....	46
31.2	EU-initiated GA suspension.....	46
ARTICLE 32 — GRANT AGREEMENT OR BENEFICIARY TERMINATION.....		47
32.1	Consortium-requested GA termination.....	47
32.2	Consortium-requested beneficiary termination.....	48
32.3	EU-initiated GA or beneficiary termination.....	49
SECTION 3 OTHER CONSEQUENCES: DAMAGES AND ADMINISTRATIVE SANCTIONS.....		53
ARTICLE 33 — DAMAGES.....		53
33.1	Liability of the granting authority.....	53
33.2	Liability of the beneficiaries.....	53
ARTICLE 34 — ADMINISTRATIVE SANCTIONS AND OTHER MEASURES.....		53
SECTION 4 FORCE MAJEURE.....		53

ARTICLE 35 — FORCE MAJEURE.....53

CHAPTER 6 FINAL PROVISIONS.....54

ARTICLE 36 — COMMUNICATION BETWEEN THE PARTIES.....54

 36.1 Forms and means of communication — Electronic management..... 54

 36.2 Date of communication..... 54

 36.3 Addresses for communication..... 54

ARTICLE 37 — INTERPRETATION OF THE AGREEMENT.....55

ARTICLE 38 — CALCULATION OF PERIODS AND DEADLINES.....55

ARTICLE 39 — AMENDMENTS..... 55

 39.1 Conditions..... 55

 39.2 Procedure..... 55

ARTICLE 40 — ACCESSION AND ADDITION OF NEW BENEFICIARIES..... 56

 40.1 Accession of the beneficiaries mentioned in the Preamble..... 56

 40.2 Addition of new beneficiaries..... 56

ARTICLE 41 — TRANSFER OF THE AGREEMENT..... 56

ARTICLE 42 — ASSIGNMENTS OF CLAIMS FOR PAYMENT AGAINST THE GRANTING
AUTHORITY.....57

ARTICLE 43 — APPLICABLE LAW AND SETTLEMENT OF DISPUTES..... 57

 43.1 Applicable law.....57

 43.2 Dispute settlement..... 57

ARTICLE 44 — ENTRY INTO FORCE.....58

DATA SHEET

1. General data

Project summary:

Project summary
The University of Ostrava (OU) in Czechia aims to build a new dormitory (block C) with a housing capacity of 332 beds next to the existing blocks A and B, mainly for students from other Czech regions and countries who represent one-third of the OU students. The project's goal is to expand the affordable student housing in the Moravian-Silesian Region, a coal region undergoing transition to a low-carbon economy. The project will address the population decline and labour market mismatch by providing social infrastructure for education and housing. It will help to prevent the youth from leaving, attract more students from other regions and abroad, and improve the local labour market, thus indirectly supporting the diversification of the local economy. The project will also contribute to sustainability by applying a building design that integrates the use of renewable energy sources and smart solutions. The new building will have low energy and water consumption as it will use geothermal heat pumps, solar panels, dichroic façade and high-quality insulation for thermoregulation, and water harvesting system. The expected energy performance score of the new building is EPC B. The project is supported by an EU grant (EUR 1.303 million) under PSLF, complemented by a loan (EUR 5.214 million) awarded by the EIB via the National Development Bank, and other national grants (EUR 12.105 million), bringing the total project budget to EUR 18.622 million.

Keywords:

- affordable student housing in structurally affected region

Project number: 101192431

Project name: Affordable student housing for the University of Ostrava

Project acronym: 2024-6-CZ-Dormitory

Call: JTM-2022-2025-PSLF

Topic: JTM-2022-2025-PSLF-STANDALONE-PROJECTS

Type of action: JTM Lump Sum Grants

Granting authority: European Climate, Infrastructure and Environment Executive Agency

Grant managed through EU Funding & Tenders Portal: Yes (eGrants)

Project starting date: fixed date: 12 June 2025

Project end date: 11 June 2027

Project duration: 24 months

Consortium agreement: Yes

2. Participants

List of participants:

N°	Role	Short name	Legal name	Ctry	PIC	Max grant amount
1	COO	OU	OSTRAVSKA UNIVERZITA	CZ	998738870	1 303 473.19
Total						1 303 473.19

Coordinator:

- OSTRAVSKA UNIVERZITA (OU)

3. Grant

Maximum grant amount, total estimated eligible costs and contributions and funding rate:

Maximum grant amount (Annex 2)	Maximum grant amount (award decision)
1 303 473.19	1 303 473.19

Grant form: Lump Sum**Grant mode:** Action grant**Budget categories/activity types:** Lump sum contributions**Cost eligibility options:** n/a**Budget flexibility:** No**4. Reporting, payments and recoveries****4.1 Continuous reporting** (art 21)**Deliverables:** see Funding & Tenders Portal Continuous Reporting tool**4.2 Periodic reporting and payments****Reporting and payment schedule** (art 21, 22):

Reporting					Payments	
Reporting periods			Type	Deadline	Type	Deadline (time to pay)
RP No	Month from	Month to				
					Initial prefinancing	30 days from entry into force/ financial guarantee (if required) – whichever is the latest
					Final payment	90 days from receiving periodic report
1	1	24	Periodic report	60 days after end of reporting period		

Prefinancing payments and guarantees:

Prefinancing payment		Prefinancing guarantee		
Type	Amount	Guarantee amount	Division per participant	
Prefinancing 1 (initial)	912 431.23	n/a	1 - OU	n/a

Reporting and payment modalities (art 21, 22):

Mutual Insurance Mechanism (MIM): No

Restrictions on distribution of initial prefinancing: The prefinancing may be distributed only if the minimum number of beneficiaries set out in the call conditions (if any) have acceded to the Agreement and only to beneficiaries that have acceded.

Interim payment ceiling (if any): 100% of the maximum grant amount

No-profit rule: n/a

Late payment interest: ECB + 3.5%

Bank account for payments:

CZ6507100000000000931761 CNBACZPP

Conversion into euros: n/a

Reporting language: Language of the Agreement

4.3 Certificates (art 24): n/a

4.4 Recoveries (art 22)

First-line liability for recoveries:

Beneficiary termination: Beneficiary concerned

Final payment: Coordinator

After final payment: Beneficiary concerned

Joint and several liability for enforced recoveries (in case of non-payment):

Limited joint and several liability of other beneficiaries — up to the maximum grant amount of the beneficiary

Joint and several liability of affiliated entities — n/a

5. Consequences of non-compliance, applicable law & dispute settlement forum

Suspension and termination:

Additional suspension grounds (art 31)

Additional termination grounds (art 32)

Applicable law (art 43):

Standard applicable law regime: EU law + law of Belgium

Dispute settlement forum (art 43):

Standard dispute settlement forum:

EU beneficiaries: EU General Court + EU Court of Justice (on appeal)

Non-EU beneficiaries: Courts of Brussels, Belgium (unless an international agreement provides for the enforceability of EU court judgements)

6. Other

Specific rules (Annex 5): Yes

Standard time-limits after project end:

Confidentiality (for X years after final payment): 5

Record-keeping (for X years after final payment): 5 (or 3 for grants of not more than EUR 60 000)

Reviews (up to X years after final payment): 5 (or 3 for grants of not more than EUR 60 000)

Audits (up to X years after final payment): 5 (or 3 for grants of not more than EUR 60 000)

Extension of findings from other grants to this grant (no later than X years after final payment): 5 (or 3 for grants of not more than EUR 60 000)

Impact evaluation (up to X years after final payment): 5 (or 3 for grants of not more than EUR 60 000)

CHAPTER 1 GENERAL

ARTICLE 1 — SUBJECT OF THE AGREEMENT

This Agreement sets out the rights and obligations and terms and conditions applicable to the grant awarded for the implementation of the action set out in Chapter 2.

ARTICLE 2 — DEFINITIONS

For the purpose of this Agreement, the following definitions apply:

Actions — The project which is being funded in the context of this Agreement.

Grant — The grant awarded in the context of this Agreement.

EU grants — Grants awarded by EU institutions, bodies, offices or agencies (including EU executive agencies, EU regulatory agencies, EDA, joint undertakings, etc.).

Participants — Entities participating in the action as beneficiaries, affiliated entities, associated partners, third parties giving in-kind contributions, subcontractors or recipients of financial support to third parties.

Beneficiaries (BEN) — The signatories of this Agreement (either directly or through an accession form).

Affiliated entities (AE) — Entities affiliated to a beneficiary within the meaning of Article 190 of EU Financial Regulation 2024/2509⁴ which participate in the action with similar rights and obligations as the beneficiaries (obligation to implement action tasks and right to charge costs and claim contributions).

Associated partners (AP) — Entities which participate in the action, but without the right to charge costs or claim contributions.

Purchases — Contracts for goods, works or services needed to carry out the action (e.g. equipment, consumables and supplies) but which are not part of the action tasks (see Annex 1).

Subcontracting — Contracts for goods, works or services that are part of the action tasks (see Annex 1).

In-kind contributions — In-kind contributions within the meaning of Article 2(38) of EU Financial Regulation 2024/2509, i.e. non-financial resources made available free of charge by third parties.

⁴ For the definition, see Article 190 Regulation (EU, Euratom) 2024/2509 of the European Parliament and of the Council of 23 September 2024 on the financial rules applicable to the general budget of the Union (recast) ('EU Financial Regulation') (OJ L, 2024/2509, 26.9.2024): "**affiliated entities** [are]:

- (a) entities that form a sole beneficiary [(i.e. where an entity is formed of several entities that satisfy the criteria for being awarded a grant, including where the entity is specifically established for the purpose of implementing an action to be financed by a grant)];
- (b) entities that satisfy the eligibility criteria and that do not fall within one of the situations referred to in Article 138(1) and 143(1) and that have a link with the beneficiary, in particular a legal or capital link, which is neither limited to the action nor established for the sole purpose of its implementation".

Fraud — Fraud within the meaning of Article 3 of EU Directive 2017/1371⁵ and Article 1 of the Convention on the protection of the European Communities' financial interests, drawn up by the Council Act of 26 July 1995⁶, as well as any other wrongful or criminal deception intended to result in financial or personal gain.

Irregularities — Any type of breach (regulatory or contractual) which could impact the EU financial interests, including irregularities within the meaning of Article 1(2) of EU Regulation 2988/95⁷.

Grave professional misconduct — Any type of unacceptable or improper behaviour in exercising one's profession, especially by employees, including grave professional misconduct within the meaning of Article 138(1)(c) of EU Financial Regulation 2024/2509⁸.

Applicable EU, international and national law — Any legal acts or other (binding or non-binding) rules and guidance in the area concerned.

Portal — EU Funding & Tenders Portal; electronic portal and exchange system managed by the European Commission and used by itself and other EU institutions, bodies, offices or agencies for the management of their funding programmes (grants, procurements, prizes, etc.).

CHAPTER 2 ACTION

ARTICLE 3 — ACTION

The grant is awarded for the action **101192431 — 2024-6-CZ-Dormitory** ('action'), as described in Annex 1.

ARTICLE 4 — DURATION AND STARTING DATE

The duration and the starting date of the action are set out in the Data Sheet (see Point 1).

CHAPTER 3 GRANT

ARTICLE 5 — GRANT

⁵ Directive (EU) 2017/1371 of the European Parliament and of the Council of 5 July 2017 on the fight against fraud to the Union's financial interests by means of criminal law (OJ L 198, 28.7.2017, p. 29).

⁶ OJ C 316, 27.11.1995, p. 48.

⁷ Council Regulation (EC, Euratom) No 2988/95 of 18 December 1995 on the protection of the European Communities financial interests (OJ L 312, 23.12.1995, p. 1).

⁸ 'Professional misconduct' includes, in particular, the following: violation of ethical standards of the profession; wrongful conduct with impact on professional credibility; breach of generally accepted professional ethical standards; false declarations/misrepresentation of information; participation in a cartel or other agreement distorting competition; violation of IPR; attempting to influence decision-making processes by taking advantage, through misrepresentation, of a conflict of interests, or to obtain confidential information from public authorities to gain an advantage; incitement to discrimination, hatred or violence or similar activities contrary to the EU values where negatively affecting or risking to affect the performance of a legal commitment.

5.1 Form of grant

The grant is an action grant⁹ which takes the form of a lump sum grant for the completion of work packages.

5.2 Maximum grant amount

The maximum grant amount is set out in the Data Sheet (see Point 3) and in the estimated budget (Annex 2).

5.3 Funding rate

Not applicable

5.4 Estimated budget, budget categories and forms of funding

The estimated budget for the action (lump sum breakdown) is set out in Annex 2.

It contains the estimated eligible contributions for the action (lump sum contributions), broken down by participant and work package.

Annex 2 also shows the types of contributions (forms of funding)¹⁰ to be used for each work package.

5.5 Budget flexibility

Budget flexibility does not apply; changes to the estimated budget (lump sum breakdown) always require an amendment (see Article 39).

Amendments for transfers between *work packages* are moreover possible only if:

- the work packages concerned are not already completed (and declared in a financial statement) and
- the transfers are justified by the technical implementation of the action.

ARTICLE 6 — ELIGIBLE AND INELIGIBLE CONTRIBUTIONS

6.1 and 6.2 General and specific eligibility conditions

Lump sum contributions are eligible ('eligible contributions'), if:

- (a) they are set out in Annex 2 and
- (b) the work packages are completed and the work is properly implemented by the beneficiaries and/or the results are achieved, in accordance with Annex 1 and during in the period set out in Article 4 (with the exception of work/results relating to the submission of the final periodic report, which may be achieved afterwards; see Article 21)

⁹ For the definition, see Article 183(2)(a) EU Financial Regulation 2024/2509: '**action grant**' means an EU grant to finance "an action intended to help achieve a Union policy objective".

¹⁰ See Article 125 EU Financial Regulation 2024/2509.

They will be calculated on the basis of the amounts set out in Annex 2.

6.3 Ineligible contributions

‘Ineligible contributions’ are:

- (a) lump sum contributions that do not comply with the conditions set out above (see Article 6.1 and 6.2)
- (b) lump sum contributions for activities already funded under other EU grants (or grants awarded by an EU Member State, non-EU country or other body implementing the EU budget), except for the following case:
 - (i) Synergy actions: not applicable
- (c) other:
 - (i) country restrictions for eligible costs: not applicable.

6.4 Consequences of non-compliance

If a beneficiary declares lump sum contributions that are ineligible, they will be rejected (see Article 27).

This may also lead to other measures described in Chapter 5.

CHAPTER 4 GRANT IMPLEMENTATION

SECTION 1 CONSORTIUM: BENEFICIARIES, AFFILIATED ENTITIES AND OTHER PARTICIPANTS

ARTICLE 7 — BENEFICIARIES

The beneficiaries, as signatories of the Agreement, are fully responsible towards the granting authority for implementing it and for complying with all its obligations.

They must implement the Agreement to their best abilities, in good faith and in accordance with all the obligations and terms and conditions it sets out.

They must have the appropriate resources to implement the action and implement the action under their own responsibility and in accordance with Article 11. If they rely on affiliated entities or other participants (see Articles 8 and 9), they retain sole responsibility towards the granting authority and the other beneficiaries.

They are jointly responsible for the *technical* implementation of the action. If one of the beneficiaries fails to implement their part of the action, the other beneficiaries must ensure that this part is implemented by someone else (without being entitled to an increase of the maximum grant amount and subject to an amendment; see Article 39). The *financial* responsibility of each beneficiary in case of recoveries is governed by Article 22.

The beneficiaries (and their action) must remain eligible under the EU programme funding the grant for the entire duration of the action. Lump sum contributions will be eligible only as long as the beneficiary and the action are eligible.

The **internal roles and responsibilities** of the beneficiaries are divided as follows:

(a) Each beneficiary must:

- (i) keep information stored in the Portal Participant Register up to date (see Article 19)
- (ii) inform the granting authority (and the other beneficiaries) immediately of any events or circumstances likely to affect significantly or delay the implementation of the action (see Article 19)
- (iii) submit to the coordinator in good time:
 - the prefinancing guarantees (if required; see Article 23)
 - the financial statements and certificates on the financial statements (CFS): not applicable
 - the contribution to the deliverables and technical reports (see Article 21)
 - any other documents or information required by the granting authority under the Agreement
- (iv) submit via the Portal data and information related to the participation of their affiliated entities.

(b) The coordinator must:

- (i) monitor that the action is implemented properly (see Article 11)
- (ii) act as the intermediary for all communications between the consortium and the granting authority, unless the Agreement or granting authority specifies otherwise, and in particular:
 - submit the prefinancing guarantees to the granting authority (if any)
 - request and review any documents or information required and verify their quality and completeness before passing them on to the granting authority
 - submit the deliverables and reports to the granting authority
 - inform the granting authority about the payments made to the other beneficiaries (report on the distribution of payments; if required, see Articles 22 and 32)
- (iii) distribute the payments received from the granting authority to the other beneficiaries without unjustified delay (see Article 22).

The coordinator may not delegate or subcontract the above-mentioned tasks to any other beneficiary or third party (including affiliated entities).

However, coordinators which are public bodies may delegate the tasks set out in Point (b)(ii) last indent and (iii) above to entities with ‘authorisation to administer’ which they have created or which are controlled by or affiliated to them. In this case, the coordinator retains sole responsibility for the payments and for compliance with the obligations under the Agreement.

Moreover, coordinators which are ‘sole beneficiaries’¹¹ (or similar, such as European research infrastructure consortia (ERICs)) may delegate the tasks set out in Point (b)(i) to (iii) above to one of their members. The coordinator retains sole responsibility for compliance with the obligations under the Agreement.

The beneficiaries must have **internal arrangements** regarding their operation and co-ordination, to ensure that the action is implemented properly.

If required by the granting authority (see Data Sheet, Point 1), these arrangements must be set out in a written **consortium agreement** between the beneficiaries, covering for instance:

- the internal organisation of the consortium
- the management of access to the Portal
- different distribution keys for the payments and financial responsibilities in case of recoveries (if any)
- additional rules on rights and obligations related to background and results (see Article 16)
- settlement of internal disputes
- liability, indemnification and confidentiality arrangements between the beneficiaries.

The internal arrangements must not contain any provision contrary to this Agreement.

ARTICLE 8 — AFFILIATED ENTITIES

Not applicable

ARTICLE 9 — OTHER PARTICIPANTS INVOLVED IN THE ACTION

9.1 Associated partners

Not applicable

9.2 Third parties giving in-kind contributions to the action

Other third parties may give in-kind contributions to the action (i.e. personnel, equipment, other goods, works and services, etc. which are free-of-charge), if necessary for the implementation.

Third parties giving in-kind contributions do not implement any action tasks. They may not charge

¹¹ For the definition, see Article 190(2) EU Financial Regulation 2024/2509: “Where several entities satisfy the criteria for being awarded a grant and together form one entity, that entity may be treated as the **sole beneficiary**, including where it is specifically established for the purpose of implementing the action financed by the grant.”

contributions to the action (no lump sum contributions) and the costs for the in-kind contributions are not eligible (may not be included in the estimated budget in Annex 2).

The third parties and their in-kind contributions should be set out in Annex 1.

9.3 Subcontractors

Subcontractors may participate in the action, if necessary for the implementation.

Subcontractors must implement their action tasks in accordance with Article 11. The beneficiaries' costs for subcontracting are considered entirely covered by the lump sum contributions for implementing the work packages (irrespective of the actual subcontracting costs incurred, if any).

The beneficiaries must ensure that their contractual obligations under Articles 11 (proper implementation), 12 (conflict of interest), 13 (confidentiality and security), 14 (ethics), 17.2 (visibility), 18 (specific rules for carrying out action), 19 (information) and 20 (record-keeping) also apply to the subcontractors.

The beneficiaries must ensure that the bodies mentioned in Article 25 (e.g. granting authority, OLAF, Court of Auditors (ECA), etc.) can exercise their rights also towards the subcontractors.

9.4 Recipients of financial support to third parties

If the action includes providing financial support to third parties (e.g. grants, prizes or similar forms of support), the beneficiaries must ensure that their contractual obligations under Articles 12 (conflict of interest), 13 (confidentiality and security), 14 (ethics), 17.2 (visibility), 18 (specific rules for carrying out action), 19 (information) and 20 (record-keeping) also apply to the third parties receiving the support (recipients).

The beneficiaries must also ensure that the bodies mentioned in Article 25 (e.g. granting authority, OLAF, Court of Auditors (ECA), etc.) can exercise their rights also towards the recipients.

ARTICLE 10 — PARTICIPANTS WITH SPECIAL STATUS

10.1 Non-EU participants

Participants which are established in a non-EU country (if any) undertake to comply with their obligations under the Agreement and:

- to respect general principles (including fundamental rights, values and ethical principles, environmental and labour standards, rules on classified information, intellectual property rights, visibility of funding and protection of personal data)
- for the submission of certificates under Article 24: use qualified external auditors which are independent and comply with comparable standards as those set out in EU Directive 2006/43/EC¹²
- for the controls under Article 25: allow for checks, reviews, audits and investigations (including

¹² Directive 2006/43/EC of the European Parliament and of the Council of 17 May 2006 on statutory audits of annual accounts and consolidated accounts (OJ L 157, 9.6.2006, p. 87).

on-the-spot checks, visits and inspections) by the bodies mentioned in that Article (e.g. granting authority, OLAF, Court of Auditors (ECA), etc.).

Special rules on dispute settlement apply (see Data Sheet, Point 5).

10.2 Participants which are international organisations

Participants which are international organisations (IOs; if any) undertake to comply with their obligations under the Agreement and:

- to respect general principles (including fundamental rights, values and ethical principles, environmental and labour standards, rules on classified information, intellectual property rights, visibility of funding and protection of personal data)
- for the submission of certificates under Article 24: to use either independent public officers or external auditors which comply with comparable standards as those set out in EU Directive 2006/43/EC¹³
- for the controls under Article 25: to allow for the checks, reviews, audits and investigations by the bodies mentioned in that Article, taking into account the specific agreements concluded by them and the EU (if any).

For such participants, nothing in the Agreement will be interpreted as a waiver of their privileges or immunities, as accorded by their constituent documents or international law.

Special rules on applicable law and dispute settlement apply (see Article 43 and Data Sheet, Point 5).

10.3 Pillar-assessed participants

Pillar-assessed participants (if any) may rely on their own systems, rules and procedures, in so far as they have been positively assessed and do not call into question the decision awarding the grant or breach the principle of equal treatment of applicants or beneficiaries.

‘Pillar-assessment’ means a review by the European Commission on the systems, rules and procedures which participants use for managing EU grants (in particular internal control system, accounting system, external audits, financing of third parties, rules on recovery and exclusion, information on recipients and protection of personal data; see Article 157 EU Financial Regulation 2024/2509).

Participants with a positive pillar assessment may rely on their own systems, rules and procedures, in particular for:

- record-keeping (Article 20): may be done in accordance with internal standards, rules and procedures
- currency conversion for financial statements (Article 21): may be done in accordance with usual accounting practices
- guarantees (Article 23): for public law bodies, prefinancing guarantees are not needed

¹³ Directive 2006/43/EC of the European Parliament and of the Council of 17 May 2006 on statutory audits of annual accounts and consolidated accounts (OJ L 157, 9.6.2006, p. 87).

- certificates (Article 24):
 - certificates on the financial statements (CFS): may be provided by their regular internal or external auditors and in accordance with their internal financial regulations and procedures
 - certificates on usual accounting practices (CoMUC): are not needed if those practices are covered by an ex-ante assessment

and use the following specific rules, for:

- recoveries (Article 22): in case of financial support to third parties, there will be no recovery if the participant has done everything possible to retrieve the undue amounts from the third party receiving the support (including legal proceedings) and non-recovery is not due to an error or negligence on its part
- checks, reviews, audits and investigations by the EU (Article 25): will be conducted taking into account the rules and procedures specifically agreed between them and the framework agreement (if any)
- impact evaluation (Article 26): will be conducted in accordance with the participant's internal rules and procedures and the framework agreement (if any)
- grant agreement termination (Article 32): the final grant amount and final payment will be calculated taking into account also costs relating to contracts due for execution only after termination takes effect, if the contract was entered into before the pre-information letter was received and could not reasonably be terminated on legal grounds
- liability for damages (Article 33.2): the granting authority must be compensated for damage it sustains as a result of the implementation of the action or because the action was not implemented in full compliance with the Agreement only if the damage is due to an infringement of the participant's internal rules and procedures or due to a violation of third parties' rights by the participant or one of its employees or individual for whom the employees are responsible.

Participants whose pillar assessment covers procurement and granting procedures may also do purchases, subcontracting and financial support to third parties (Article 6.2) in accordance with their internal rules and procedures for purchases, subcontracting and financial support.

Participants whose pillar assessment covers data protection rules may rely on their internal standards, rules and procedures for data protection (Article 15).

The participants may however not rely on provisions which would breach the principle of equal treatment of applicants or beneficiaries or call into question the decision awarding the grant, such as in particular:

- eligibility (Article 6)
- consortium roles and set-up (Articles 7-9)
- security and ethics (Articles 13, 14)

- IPR (including background and results, access rights and rights of use), communication, dissemination and visibility (Articles 16 and 17)
- information obligation (Article 19)
- payment, reporting and amendments (Articles 21, 22 and 39)
- rejections, reductions, suspensions and terminations (Articles 27, 28, 29-32)

If the pillar assessment was subject to remedial measures, reliance on the internal systems, rules and procedures is subject to compliance with those remedial measures.

Participants must inform the coordinator without delay of any changes to the systems, rules and procedures that were part of the pillar assessment. The coordinator must immediately inform the granting authority.

Pillar-assessed participants that have also concluded a framework agreement with the EU, may moreover — under the same conditions as those above (i.e. not call into question the decision awarding the grant or breach the principle of equal treatment of applicants or beneficiaries) — rely on provisions set out in that framework agreement.

SECTION 2 RULES FOR CARRYING OUT THE ACTION

ARTICLE 11 — PROPER IMPLEMENTATION OF THE ACTION

11.1 Obligation to properly implement the action

The beneficiaries must implement the action as described in Annex 1 and in compliance with the provisions of the Agreement, the call conditions and all legal obligations under applicable EU, international and national law.

11.2 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 12 — CONFLICT OF INTERESTS

12.1 Conflict of interests

The beneficiaries must take all measures to prevent any situation where the impartial and objective implementation of the Agreement could be compromised for reasons involving family, emotional life, political or national affinity, economic interest or any other direct or indirect interest ('conflict of interests').

They must formally notify the granting authority without delay of any situation constituting or likely to lead to a conflict of interests and immediately take all the necessary steps to rectify this situation.

The granting authority may verify that the measures taken are appropriate and may require additional measures to be taken by a specified deadline.

12.2 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28) and the grant or the beneficiary may be terminated (see Article 32).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 13 — CONFIDENTIALITY AND SECURITY

13.1 Sensitive information

The parties must keep confidential any data, documents or other material (in any form) that is identified as sensitive in writing ('sensitive information') — during the implementation of the action and for at least until the time-limit set out in the Data Sheet (see Point 6).

If a beneficiary requests, the granting authority may agree to keep such information confidential for a longer period.

Unless otherwise agreed between the parties, they may use sensitive information only to implement the Agreement.

The beneficiaries may disclose sensitive information to their personnel or other participants involved in the action only if they:

- (a) need to know it in order to implement the Agreement and
- (b) are bound by an obligation of confidentiality.

The granting authority may disclose sensitive information to its staff and to other EU institutions and bodies.

It may moreover disclose sensitive information to third parties, if:

- (a) this is necessary to implement the Agreement or safeguard the EU financial interests and
- (b) the recipients of the information are bound by an obligation of confidentiality.

The confidentiality obligations no longer apply if:

- (a) the disclosing party agrees to release the other party
- (b) the information becomes publicly available, without breaching any confidentiality obligation
- (c) the disclosure of the sensitive information is required by EU, international or national law.

Specific confidentiality rules (if any) are set out in Annex 5.

13.2 Classified information

The parties must handle classified information in accordance with the applicable EU, international or national law on classified information (in particular, Decision 2015/444¹⁴ and its implementing rules).

Deliverables which contain classified information must be submitted according to special procedures agreed with the granting authority.

Action tasks involving classified information may be subcontracted only after explicit approval (in writing) from the granting authority.

Classified information may not be disclosed to any third party (including participants involved in the action implementation) without prior explicit written approval from the granting authority.

Specific security rules (if any) are set out in Annex 5.

13.3 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 14 — ETHICS AND VALUES

14.1 Ethics

The action must be carried out in line with the highest ethical standards and the applicable EU, international and national law on ethical principles.

Specific ethics rules (if any) are set out in Annex 5.

14.2 Values

The beneficiaries must commit to and ensure the respect of basic EU values (such as respect for human dignity, freedom, democracy, equality, the rule of law and human rights, including the rights of minorities).

Specific rules on values (if any) are set out in Annex 5.

14.3 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 15 — DATA PROTECTION

15.1 Data processing by the granting authority

¹⁴ Commission Decision 2015/444/EC, Euratom of 13 March 2015 on the security rules for protecting EU classified information (OJ L 72, 17.3.2015, p. 53).

Any personal data under the Agreement will be processed under the responsibility of the data controller of the granting authority in accordance with and for the purposes set out in the Portal Privacy Statement.

For grants where the granting authority is the European Commission, an EU regulatory or executive agency, joint undertaking or other EU body, the processing will be subject to Regulation 2018/1725¹⁵.

15.2 Data processing by the beneficiaries

The beneficiaries must process personal data under the Agreement in compliance with the applicable EU, international and national law on data protection (in particular, Regulation 2016/679¹⁶).

They must ensure that personal data is:

- processed lawfully, fairly and in a transparent manner in relation to the data subjects
- collected for specified, explicit and legitimate purposes and not further processed in a manner that is incompatible with those purposes
- adequate, relevant and limited to what is necessary in relation to the purposes for which they are processed
- accurate and, where necessary, kept up to date
- kept in a form which permits identification of data subjects for no longer than is necessary for the purposes for which the data is processed and
- processed in a manner that ensures appropriate security of the data.

The beneficiaries may grant their personnel access to personal data only if it is strictly necessary for implementing, managing and monitoring the Agreement. The beneficiaries must ensure that the personnel is under a confidentiality obligation.

The beneficiaries must inform the persons whose data are transferred to the granting authority and provide them with the Portal Privacy Statement.

15.3 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 16 — INTELLECTUAL PROPERTY RIGHTS (IPR) — BACKGROUND AND RESULTS — ACCESS RIGHTS AND RIGHTS OF USE

¹⁵ Regulation (EU) 2018/1725 of the European Parliament and of the Council of 23 October 2018 on the protection of natural persons with regard to the processing of personal data by the Union institutions, bodies, offices and agencies and on the free movement of such data, and repealing Regulation (EC) No 45/2001 and Decision No 1247/2002/EC (OJ L 295, 21.11.2018, p. 39).

¹⁶ Regulation (EU) 2016/679 of the European Parliament and of the Council of 27 April 2016 on the protection of natural persons with regard to the processing of personal data and on the free movement of such data, and repealing Directive 95/46/EC ('GDPR') (OJ L 119, 4.5.2016, p. 1).

16.1 Background and access rights to background

The beneficiaries must give each other and the other participants access to the background identified as needed for implementing the action, subject to any specific rules in Annex 5.

‘Background’ means any data, know-how or information — whatever its form or nature (tangible or intangible), including any rights such as intellectual property rights — that is:

- (a) held by the beneficiaries before they acceded to the Agreement and
- (b) needed to implement the action or exploit the results.

If background is subject to rights of a third party, the beneficiary concerned must ensure that it is able to comply with its obligations under the Agreement.

16.2 Ownership of results

The granting authority does not obtain ownership of the results produced under the action.

‘Results’ means any tangible or intangible effect of the action, such as data, know-how or information, whatever its form or nature, whether or not it can be protected, as well as any rights attached to it, including intellectual property rights.

16.3 Rights of use of the granting authority on materials, documents and information received for policy, information, communication, dissemination and publicity purposes

The granting authority has the right to use non-sensitive information relating to the action and materials and documents received from the beneficiaries (notably summaries for publication, deliverables, as well as any other material, such as pictures or audio-visual material, in paper or electronic form) for policy information, communication, dissemination and publicity purposes — during the action or afterwards.

The right to use the beneficiaries’ materials, documents and information is granted in the form of a royalty-free, non-exclusive and irrevocable licence, which includes the following rights:

- (a) **use for its own purposes** (in particular, making them available to persons working for the granting authority or any other EU service (including institutions, bodies, offices, agencies, etc.) or EU Member State institution or body; copying or reproducing them in whole or in part, in unlimited numbers; and communication through press information services)
- (b) **distribution to the public** (in particular, publication as hard copies and in electronic or digital format, publication on the internet, as a downloadable or non-downloadable file, broadcasting by any channel, public display or presentation, communicating through press information services, or inclusion in widely accessible databases or indexes)
- (c) **editing or redrafting** (including shortening, summarising, inserting other elements (e.g. meta-data, legends, other graphic, visual, audio or text elements), extracting parts (e.g. audio or video files), dividing into parts, use in a compilation)
- (d) **translation**
- (e) **storage** in paper, electronic or other form

- (f) **archiving**, in line with applicable document-management rules
- (g) the right to authorise **third parties** to act on its behalf or sub-license to third parties the modes of use set out in Points (b), (c), (d) and (f), if needed for the information, communication and publicity activity of the granting authority and
- (h) **processing**, analysing, aggregating the materials, documents and information received and **producing derivative works**.

The rights of use are granted for the whole duration of the industrial or intellectual property rights concerned.

If materials or documents are subject to moral rights or third party rights (including intellectual property rights or rights of natural persons on their image and voice), the beneficiaries must ensure that they comply with their obligations under this Agreement (in particular, by obtaining the necessary licences and authorisations from the rights holders concerned).

Where applicable, the granting authority will insert the following information:

“© – [year] – [name of the copyright owner]. All rights reserved. Licensed to the [name of granting authority] under conditions.”

16.4 Specific rules on IPR, results and background

Specific rules regarding intellectual property rights, results and background (if any) are set out in Annex 5.

16.5 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such a breach may also lead to other measures described in Chapter 5.

ARTICLE 17 — COMMUNICATION, DISSEMINATION AND VISIBILITY

17.1 Communication — Dissemination — Promoting the action

Unless otherwise agreed with the granting authority, the beneficiaries must promote the action and its results by providing targeted information to multiple audiences (including the media and the public), in accordance with Annex 1 and in a strategic, coherent and effective manner.

Before engaging in a communication or dissemination activity expected to have a major media impact, the beneficiaries must inform the granting authority.

17.2 Visibility — European flag and funding statement

Unless otherwise agreed with the granting authority, communication activities of the beneficiaries related to the action (including media relations, conferences, seminars, information material, such as brochures, leaflets, posters, presentations, etc., in electronic form, via traditional or social media, etc.), dissemination activities and any infrastructure, equipment, vehicles, supplies or major result funded

by the grant must acknowledge the EU support and display the European flag (emblem) and funding statement (translated into local languages, where appropriate):



Funded by the
European Union



Co-funded by the
European Union



Funded by the
European Union



Co-funded by the
European Union

The emblem must remain distinct and separate and cannot be modified by adding other visual marks, brands or text.

Apart from the emblem, no other visual identity or logo may be used to highlight the EU support.

When displayed in association with other logos (e.g. of beneficiaries or sponsors), the emblem must be displayed at least as prominently and visibly as the other logos.

For the purposes of their obligations under this Article, the beneficiaries may use the emblem without first obtaining approval from the granting authority. This does not, however, give them the right to exclusive use. Moreover, they may not appropriate the emblem or any similar trademark or logo, either by registration or by any other means.

17.3 Quality of information — Disclaimer

Any communication or dissemination activity related to the action must use factually accurate information.

Moreover, it must indicate the following disclaimer (translated into local languages where appropriate):

“Funded by the European Union. Views and opinions expressed are however those of the author(s) only and do not necessarily reflect those of the European Union or [name of the granting authority]. Neither the European Union nor the granting authority can be held responsible for them.”

17.4 Specific communication, dissemination and visibility rules

Specific communication, dissemination and visibility rules (if any) are set out in Annex 5.

17.5 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 18 — SPECIFIC RULES FOR CARRYING OUT THE ACTION

18.1 Specific rules for carrying out the action

Specific rules for implementing the action (if any) are set out in Annex 5.

18.2 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such a breach may also lead to other measures described in Chapter 5.

SECTION 3 GRANT ADMINISTRATION

ARTICLE 19 — GENERAL INFORMATION OBLIGATIONS

19.1 Information requests

The beneficiaries must provide — during the action or afterwards and in accordance with Article 7 — any information requested in order to verify eligibility of the lump sum contributions declared, proper implementation of the action and compliance with the other obligations under the Agreement.

The information provided must be accurate, precise and complete and in the format requested, including electronic format.

19.2 Participant Register data updates

The beneficiaries must keep — at all times, during the action or afterwards — their information stored in the Portal Participant Register up to date, in particular, their name, address, legal representatives, legal form and organisation type.

19.3 Information about events and circumstances which impact the action

The beneficiaries must immediately inform the granting authority (and the other beneficiaries) of any of the following:

- (a) **events** which are likely to affect or delay the implementation of the action or affect the EU's financial interests, in particular:
 - (i) changes in their legal, financial, technical, organisational or ownership situation (including changes linked to one of the exclusion grounds listed in the declaration of honour signed before grant signature)

(ii) linked action information: not applicable

(b) circumstances affecting:

(i) the decision to award the grant or

(ii) compliance with requirements under the Agreement.

19.4 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 20 — RECORD-KEEPING

20.1 Keeping records and supporting documents

The beneficiaries must — at least until the time-limit set out in the Data Sheet (see Point 6) — keep records and other supporting documents to prove the proper implementation of the action (proper implementation of the work and/or achievement of the results as described in Annex 1) in line with the accepted standards in the respective field (if any); beneficiaries do not need to keep specific records on the actual costs incurred.

The records and supporting documents must be made available upon request (see Article 19) or in the context of checks, reviews, audits or investigations (see Article 25).

If there are on-going checks, reviews, audits, investigations, litigation or other pursuits of claims under the Agreement (including the extension of findings; see Article 25), the beneficiaries must keep these records and other supporting documentation until the end of these procedures.

The beneficiaries must keep the original documents. Digital and digitalised documents are considered originals if they are authorised by the applicable national law. The granting authority may accept non-original documents if they offer a comparable level of assurance.

20.2 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, lump sum contributions insufficiently substantiated will be ineligible (see Article 6) and will be rejected (see Article 27), and the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 21 — REPORTING

21.1 Continuous reporting

The beneficiaries must report on the progress of the action (e.g. **deliverables, milestones, outputs/outcomes, critical risks, indicators**, etc; if any), in the Portal Continuous Reporting tool and in accordance with the timing and conditions it sets out (as agreed with the granting authority).

Standardised deliverables (e.g. progress reports not linked to payments, reports on cumulative expenditure, special reports, etc; if any) must be submitted using the templates published on the Portal.

21.2 Periodic reporting: Technical reports and financial statements

In addition, the beneficiaries must provide reports to request payments, in accordance with the schedule and modalities set out in the Data Sheet (see Point 4.2):

- for additional prefinancings (if any): **an additional prefinancing report**
- for interim payments (if any) and the final payment: a **periodic report**

The prefinancing and periodic reports include a technical and financial part.

The technical part includes an overview of the action implementation. It must be prepared using the template available in the Portal Periodic Reporting tool.

The financial part of the additional prefinancing report includes a statement on the use of the previous prefinancing payment.

The financial part of the periodic report includes:

- the financial statement (consolidated statement for the consortium)
- the explanation on the use of resources (or detailed cost reporting table): not applicable
- the certificates on the financial statements (CFS): not applicable.

The **financial statement** must contain the lump sum contributions indicated in Annex 2, for the work packages that were completed during the reporting period.

For the last reporting period, the beneficiaries may exceptionally also declare partial lump sum contributions for work packages that were not completed (e.g. due to force majeure or technical impossibility).

Lump sum contributions which are not declared in a financial statement will not be taken into account by the granting authority.

By signing the financial statement (directly in the Portal Periodic Reporting tool), the coordinator confirms (on behalf of the consortium) that:

- the information provided is complete, reliable and true
- the lump sum contributions declared are eligible (in particular, the work packages have been completed, that the work has been properly implemented and/or the results were achieved in accordance with Annex 1; see Article 6)
- the proper implementation and/or achievement can be substantiated by adequate records and supporting documents (see Article 20) that will be produced upon request (see Article 19) or in the context of checks, reviews, audits and investigations (see Article 25).

In case of recoveries (see Article 22), beneficiaries will be held responsible also for the lump sum contributions declared for their affiliated entities (if any).

21.3 Currency for financial statements and conversion into euros

The financial statements must be drafted in euro.

21.4 Reporting language

The reporting must be in the language of the Agreement, unless otherwise agreed with the granting authority (see Data Sheet, Point 4.2).

21.5 Consequences of non-compliance

If a report submitted does not comply with this Article, the granting authority may suspend the payment deadline (see Article 29) and apply other measures described in Chapter 5.

If the coordinator breaches its reporting obligations, the granting authority may terminate the grant or the coordinator's participation (see Article 32) or apply other measures described in Chapter 5.

ARTICLE 22 — PAYMENTS AND RECOVERIES — CALCULATION OF AMOUNTS DUE

22.1 Payments and payment arrangements

Payments will be made in accordance with the schedule and modalities set out in the Data Sheet (see Point 4.2).

They will be made in euro to the bank account indicated by the coordinator (see Data Sheet, Point 4.2) and must be distributed without unjustified delay (restrictions may apply to distribution of the initial prefinancing payment; see Data Sheet, Point 4.2).

Payments to this bank account will discharge the granting authority from its payment obligation.

The cost of payment transfers will be borne as follows:

- the granting authority bears the cost of transfers charged by its bank
- the beneficiary bears the cost of transfers charged by its bank
- the party causing a repetition of a transfer bears all costs of the repeated transfer.

Payments by the granting authority will be considered to have been carried out on the date when they are debited to its account.

22.2 Recoveries

Recoveries will be made, if — at beneficiary termination, final payment or afterwards — it turns out that the granting authority has paid too much and needs to recover the amounts undue.

The general liability regime for recoveries (first-line liability) is as follows: At final payment, the coordinator will be fully liable for recoveries, even if it has not been the final recipient of the undue amounts. At beneficiary termination or after final payment, recoveries will be made directly against the beneficiaries concerned.

Beneficiaries will be fully liable for repaying the debts of their affiliated entities.

In case of enforced recoveries (see Article 22.4):

- the beneficiaries will be jointly and severally liable for repaying debts of another beneficiary under the Agreement (including late-payment interest), if required by the granting authority (see Data Sheet, Point 4.4)
- affiliated entities will be held liable for repaying debts of their beneficiaries under the Agreement (including late-payment interest), if required by the granting authority (see Data Sheet, Point 4.4).

22.3 Amounts due

22.3.1 Prefinancing payments

The aim of the prefinancing is to provide the beneficiaries with a float.

It remains the property of the EU until the final payment.

For **initial prefinancings** (if any), the amount due, schedule and modalities are set out in the Data Sheet (see Point 4.2).

For **additional prefinancings** (if any), the amount due, schedule and modalities are also set out in the Data Sheet (see Point 4.2). However, if the statement on the use of the previous prefinancing payment shows that less than 70% was used, the amount set out in the Data Sheet will be reduced by the difference between the 70% threshold and the amount used.

Prefinancing payments (or parts of them) may be offset (without the beneficiaries' consent) against amounts owed by a beneficiary to the granting authority — up to the amount due to that beneficiary.

For grants where the granting authority is the European Commission or an EU executive agency, offsetting may also be done against amounts owed to other Commission services or executive agencies.

Payments will not be made if the payment deadline or payments are suspended (see Articles 29 and 30).

22.3.2 Amount due at beneficiary termination — Recovery

In case of beneficiary termination, the granting authority will determine the provisional amount due for the beneficiary concerned.

This will be done on the basis of work packages already completed in previous interim payments. Payments for ongoing/not yet completed work packages which the beneficiary was working on before termination (if any) will therefore be made only later on, with the next interim or final payments when those work packages have been completed.

The **amount due** will be calculated in the following step:

Step 1 — Calculation of the total accepted EU contribution

Step 1 — Calculation of the total accepted EU contribution

The granting authority will first calculate the ‘accepted EU contribution’ for the beneficiary, on the basis of the beneficiary’s lump sum contributions for the work packages which were approved in previous interim payments.

After that, the granting authority will take into account grant reductions (if any). The resulting amount is the ‘total accepted EU contribution’ for the beneficiary.

The **balance** is then calculated by deducting the payments received (if any; see report on the distribution of payments in Article 32), from the total accepted EU contribution:

$$\begin{aligned} &\{\text{total accepted EU contribution for the beneficiary} \\ &\text{minus} \\ &\{\text{prefinancing and interim payments received (if any)}\}\}. \end{aligned}$$

If the balance is **negative**, it will be **recovered** in accordance with the following procedure:

The granting authority will send a **pre-information letter** to the beneficiary concerned:

- formally notifying the intention to recover, the amount due, the amount to be recovered and the reasons why and
- requesting observations within 30 days of receiving notification.

If no observations are submitted (or the granting authority decides to pursue recovery despite the observations it has received), it will confirm the amount to be recovered and ask this amount to be paid to the coordinator (**confirmation letter**).

22.3.3 Interim payments

Interim payments reimburse the eligible lump sum contributions claimed for work packages implemented during the reporting periods (if any).

Interim payments (if any) will be made in accordance with the schedule and modalities set out the Data Sheet (see Point 4.2).

Payment is subject to the approval of the periodic report and the work packages declared. Their approval does not imply recognition of compliance, authenticity, completeness or correctness of their content.

Incomplete work packages and work packages that have not been delivered or cannot be approved will be rejected (see Article 27).

The **interim payment** will be calculated by the granting authority in the following steps:

Step 1 — Calculation of the total accepted EU contribution

Step 2 — Limit to the interim payment ceiling

Step 1 — Calculation of the total accepted EU contribution

The granting authority will first calculate the ‘accepted EU contribution’ for the action for the reporting period, by calculating the lump sum contributions for the approved work packages.

After that, the granting authority will take into account grant reductions from beneficiary termination (if any). The resulting amount is the ‘total accepted EU contribution’.

Step 2 — Limit to the interim payment ceiling

The resulting amount is then capped to ensure that the total amount of prefinancing and interim payments (if any) does not exceed the interim payment ceiling set out in the Data Sheet (see Point 4.2).

Interim payments (or parts of them) may be offset (without the beneficiaries’ consent) against amounts owed by a beneficiary to the granting authority — up to the amount due to that beneficiary.

For grants where the granting authority is the European Commission or an EU executive agency, offsetting may also be done against amounts owed to other Commission services or executive agencies.

Payments will not be made if the payment deadline or payments are suspended (see Articles 29 and 30).

22.3.4 Final payment — Final grant amount — Revenues and Profit — Recovery

The final payment (payment of the balance) reimburses the remaining eligible lump sum contributions claimed for the implemented work packages (if any).

The final payment will be made in accordance with the schedule and modalities set out in the Data Sheet (see Point 4.2).

Payment is subject to the approval of the final periodic report and the work packages declared. Their approval does not imply recognition of compliance, authenticity, completeness or correctness of their content.

Work packages (or parts of them) that have not been delivered or cannot be approved will be rejected (see Article 27).

The **final grant amount for the action** will be calculated in the following steps:

Step 1 — Calculation of the total accepted EU contribution

Step 2 — Limit to the maximum grant amount

Step 3 — Reduction due to the no-profit rule

Step 1 — Calculation of the total accepted EU contribution

The granting authority will first calculate the ‘accepted EU contribution’ for the action for all reporting periods, by calculating the lump sum contributions for the approved work packages.

After that, the granting authority will take into account grant reductions (if any). The resulting amount is the ‘total accepted EU contribution’.

Step 2 — Limit to the maximum grant amount

Not applicable

Step 3 — Reduction due to the no-profit rule

Not applicable

The **balance** (final payment) is then calculated by deducting the total amount of prefinancing and interim payments already made (if any), from the final grant amount:

$$\begin{aligned} & \{\text{final grant amount} \\ & \text{minus} \\ & \{\text{prefinancing and interim payments made (if any)}\} \}. \end{aligned}$$

If the balance is **positive**, it will be **paid** to the coordinator.

The final payment (or part of it) may be offset (without the beneficiaries' consent) against amounts owed by a beneficiary to the granting authority — up to the amount due to that beneficiary.

For grants where the granting authority is the European Commission or an EU executive agency, offsetting may also be done against amounts owed to other Commission services or executive agencies.

Payments will not be made if the payment deadline or payments are suspended (see Articles 29 and 30).

If the balance is **negative**, it will be **recovered** in accordance with the following procedure:

The granting authority will send a **pre-information letter** to the coordinator:

- formally notifying the intention to recover, the final grant amount, the amount to be recovered and the reasons why
- requesting observations within 30 days of receiving notification.

If no observations are submitted (or the granting authority decides to pursue recovery despite the observations it has received), it will confirm the amount to be recovered (**confirmation letter**), together with a **debit note** with the terms and date for payment.

If payment is not made by the date specified in the debit note, the granting authority will **enforce recovery** in accordance with Article 22.4.

22.3.5 Audit implementation after final payment — Revised final grant amount — Recovery

If — after the final payment (in particular, after checks, reviews, audits or investigations; see Article 25) — the granting authority rejects lump sum contributions (see Article 27) or reduces the grant (see Article 28), it will calculate the **revised final grant amount** for the beneficiary concerned.

The **beneficiary revised final grant amount** will be calculated in the following step:

Step 1 — Calculation of the revised total accepted EU contribution

Step 1 — Calculation of the revised total accepted EU contribution

The granting authority will first calculate the ‘revised accepted EU contribution’ for the beneficiary, by calculating the ‘revised accepted contributions’.

After that, it will take into account grant reductions (if any). The resulting ‘revised total accepted EU contribution’ is the beneficiary revised final grant amount.

If the revised final grant amount is lower than the beneficiary’s final grant amount (i.e. its share in the final grant amount for the action), it will be **recovered** in accordance with the following procedure:

The **beneficiary final grant amount** (i.e. share in the final grant amount for the action) is calculated as follows:

$$\left\{ \begin{array}{l} \text{total accepted EU contribution for the beneficiary} \\ \text{divided by} \\ \text{total accepted EU contribution for the action} \end{array} \right\} \times \left\{ \begin{array}{l} \text{multiplied by} \\ \text{final grant amount for the action} \end{array} \right\}.$$

The granting authority will send a **pre-information letter** to the beneficiary concerned:

- formally notifying the intention to recover, the amount to be recovered and the reasons why and
- requesting observations within 30 days of receiving notification.

If no observations are submitted (or the granting authority decides to pursue recovery despite the observations it has received), it will confirm the amount to be recovered (**confirmation letter**), together with a **debit note** with the terms and the date for payment.

Recoveries against affiliated entities (if any) will be handled through their beneficiaries.

If payment is not made by the date specified in the debit note, the granting authority will **enforce recovery** in accordance with Article 22.4.

22.4 Enforced recovery

If payment is not made by the date specified in the debit note, the amount due will be recovered:

- (a) by offsetting the amount — without the coordinator or beneficiary’s consent — against any amounts owed to the coordinator or beneficiary by the granting authority.

In exceptional circumstances, to safeguard the EU financial interests, the amount may be offset before the payment date specified in the debit note.

For grants where the granting authority is the European Commission or an EU executive agency, debts may also be offset against amounts owed by other Commission services or executive agencies.

- (b) by drawing on the financial guarantee(s) (if any)

- (c) by holding other beneficiaries jointly and severally liable (if any; see Data Sheet, Point 4.4)

- (d) by holding affiliated entities jointly and severally liable (if any, see Data Sheet, Point 4.4)
- (e) by taking legal action (see Article 43) or, provided that the granting authority is the European Commission or an EU executive agency, by adopting an enforceable decision under Article 299 of the Treaty on the Functioning of the EU (TFEU) and Article 100(2) of EU Financial Regulation 2024/2509.

The amount to be recovered will be increased by **late-payment interest** at the rate set out in Article 23.5, from the day following the payment date in the debit note, up to and including the date the full payment is received.

Partial payments will be first credited against expenses, charges and late-payment interest and then against the principal.

Bank charges incurred in the recovery process will be borne by the beneficiary, unless Directive 2015/2366¹⁷ applies.

For grants where the granting authority is an EU executive agency, enforced recovery by offsetting or enforceable decision will be done by the services of the European Commission (see also Article 43).

22.5 Consequences of non-compliance

22.5.1 If the granting authority does not pay within the payment deadlines (see above), the beneficiaries are entitled to **late-payment interest** at the reference rate applied by the European Central Bank (ECB) for its main refinancing operations in euros, plus the percentage specified in the Data Sheet (Point 4.2). The ECB reference rate to be used is the rate in force on the first day of the month in which the payment deadline expires, as published in the C series of the *Official Journal of the European Union*.

If the late-payment interest is lower than or equal to EUR 200, it will be paid to the coordinator only on request submitted within two months of receiving the late payment.

Late-payment interest is not due if all beneficiaries are EU Member States (including regional and local government authorities or other public bodies acting on behalf of a Member State for the purpose of this Agreement).

If payments or the payment deadline are suspended (see Articles 29 and 30), payment will not be considered as late.

Late-payment interest covers the period running from the day following the due date for payment (see above), up to and including the date of payment.

Late-payment interest is not considered for the purposes of calculating the final grant amount.

22.5.2 If the coordinator breaches any of its obligations under this Article, the grant may be reduced (see Article 28) and the grant or the coordinator may be terminated (see Article 32).

Such breaches may also lead to other measures described in Chapter 5.

¹⁷ Directive (EU) 2015/2366 of the European Parliament and of the Council of 25 November 2015 on payment services in the internal market, amending Directives 2002/65/EC, 2009/110/EC and 2013/36/EU and Regulation (EU) No 1093/2010, and repealing Directive 2007/64/EC (OJ L 337, 23.12.2015, p. 35).

ARTICLE 23 — GUARANTEES

23.1 Prefinancing guarantee

If required by the granting authority (see Data Sheet, Point 4.2), the beneficiaries must provide (one or more) prefinancing guarantee(s) in accordance with the timing and the amounts set out in the Data Sheet.

The coordinator must submit them to the granting authority in due time before the prefinancing they are linked to.

The guarantees must be drawn up using the template published on the Portal and fulfil the following conditions:

- (a) be provided by a bank or approved financial institution established in the EU or — if requested by the coordinator and accepted by the granting authority — by a third party or a bank or financial institution established outside the EU offering equivalent security
- (b) the guarantor stands as first-call guarantor and does not require the granting authority to first have recourse against the principal debtor (i.e. the beneficiary concerned) and
- (c) remain explicitly in force until the final payment and, if the final payment takes the form of a recovery, until five months after the debit note is notified to a beneficiary.

They will be released within the following month.

23.2 Consequences of non-compliance

If the beneficiaries breach their obligation to provide the prefinancing guarantee, the prefinancing will not be paid.

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 24 — CERTIFICATES

Not applicable

ARTICLE 25 — CHECKS, REVIEWS, AUDITS AND INVESTIGATIONS — EXTENSION OF FINDINGS

25.1 Granting authority checks, reviews and audits

25.1.1 Internal checks

The granting authority may — during the action or afterwards — check the proper implementation of the action and compliance with the obligations under the Agreement, including assessing lump sum contributions, deliverables and reports.

25.1.2 Project reviews

The granting authority may carry out reviews on the proper implementation of the action and

compliance with the obligations under the Agreement (general project reviews or specific issues reviews).

Such project reviews may be started during the implementation of the action and until the time-limit set out in the Data Sheet (see Point 6). They will be formally notified to the coordinator or beneficiary concerned and will be considered to start on the date of the notification.

If needed, the granting authority may be assisted by independent, outside experts. If it uses outside experts, the coordinator or beneficiary concerned will be informed and have the right to object on grounds of commercial confidentiality or conflict of interest.

The coordinator or beneficiary concerned must cooperate diligently and provide — within the deadline requested — any information and data in addition to deliverables and reports already submitted. The granting authority may request beneficiaries to provide such information to it directly. Sensitive information and documents will be treated in accordance with Article 13.

The coordinator or beneficiary concerned may be requested to participate in meetings, including with the outside experts.

For **on-the-spot visits**, the beneficiary concerned must allow access to sites and premises (including to the outside experts) and must ensure that information requested is readily available.

Information provided must be accurate, precise and complete and in the format requested, including electronic format.

On the basis of the review findings, a **project review report** will be drawn up.

The granting authority will formally notify the project review report to the coordinator or beneficiary concerned, which has 30 days from receiving notification to make observations.

Project reviews (including project review reports) will be in the language of the Agreement, unless otherwise agreed with the granting authority (see Data Sheet, Point 4.2).

25.1.3 Audits

The granting authority may carry out audits on the proper implementation of the action and compliance with the obligations under the Agreement.

Such audits may be started during the implementation of the action and until the time-limit set out in the Data Sheet (see Point 6). They will be formally notified to the beneficiary concerned and will be considered to start on the date of the notification.

The granting authority may use its own audit service, delegate audits to a centralised service or use external audit firms. If it uses an external firm, the beneficiary concerned will be informed and have the right to object on grounds of commercial confidentiality or conflict of interest.

The beneficiary concerned must cooperate diligently and provide — within the deadline requested — any information (including complete accounts, individual salary statements or other personal data) to verify compliance with the Agreement. Sensitive information and documents will be treated in accordance with Article 13.

For **on-the-spot** visits, the beneficiary concerned must allow access to sites and premises (including for the external audit firm) and must ensure that information requested is readily available.

Information provided must be accurate, precise and complete and in the format requested, including electronic format.

On the basis of the audit findings, a **draft audit report** will be drawn up.

The auditors will formally notify the draft audit report to the beneficiary concerned, which has 30 days from receiving notification to make observations (contradictory audit procedure).

The **final audit report** will take into account observations by the beneficiary concerned and will be formally notified to them.

Audits (including audit reports) will be in the language of the Agreement, unless otherwise agreed with the granting authority (see Data Sheet, Point 4.2).

25.2 European Commission checks, reviews and audits in grants of other granting authorities

Where the granting authority is not the European Commission, the latter has the same rights of checks, reviews and audits as the granting authority.

25.3 Access to records for assessing simplified forms of funding

The beneficiaries must give the European Commission access to their statutory records for the periodic assessment of simplified forms of funding which are used in EU programmes.

25.4 OLAF, EPPO and ECA audits and investigations

The following bodies may also carry out checks, reviews, audits and investigations — during the action or afterwards:

- the European Anti-Fraud Office (OLAF) under Regulations No 883/2013¹⁸ and No 2185/96¹⁹
- the European Public Prosecutor's Office (EPPO) under Regulation 2017/1939
- the European Court of Auditors (ECA) under Article 287 of the Treaty on the Functioning of the EU (TFEU) and Article 263 of EU Financial Regulation 2024/2509.

If requested by these bodies, the beneficiary concerned must provide full, accurate and complete information in the format requested (including complete accounts, individual salary statements or other personal data, including in electronic format) and allow access to sites and premises for on-the-spot visits or inspections — as provided for under these Regulations.

¹⁸ Regulation (EU, Euratom) No 883/2013 of the European Parliament and of the Council of 11 September 2013 concerning investigations conducted by the European Anti-Fraud Office (OLAF) and repealing Regulation (EC) No 1073/1999 of the European Parliament and of the Council and Council Regulation (Euratom) No 1074/1999 (OJ L 248, 18/09/2013, p. 1).

¹⁹ Council Regulation (Euratom, EC) No 2185/96 of 11 November 1996 concerning on-the-spot checks and inspections carried out by the Commission in order to protect the European Communities' financial interests against fraud and other irregularities (OJ L 292, 15/11/1996, p. 2).

To this end, the beneficiary concerned must keep all relevant information relating to the action, at least until the time-limit set out in the Data Sheet (Point 6) and, in any case, until any ongoing checks, reviews, audits, investigations, litigation or other pursuits of claims have been concluded.

25.5 Consequences of checks, reviews, audits and investigations — Extension of findings

25.5.1 Consequences of checks, reviews, audits and investigations in this grant

Findings in checks, reviews, audits or investigations carried out in the context of this grant may lead to rejections (see Article 27), grant reduction (see Article 28) or other measures described in Chapter 5.

Rejections or grant reductions after the final payment will lead to a revised final grant amount (see Article 22).

Findings in checks, reviews, audits or investigations during the action implementation may lead to a request for amendment (see Article 39), to change the description of the action set out in Annex 1.

Checks, reviews, audits or investigations that find systemic or recurrent errors, irregularities, fraud or breach of obligations in any EU grant may also lead to consequences in other EU grants awarded under similar conditions ('extension to other grants').

Moreover, findings arising from an OLAF or EPPO investigation may lead to criminal prosecution under national law.

25.5.2 Extension from other grants

Findings of checks, reviews, audits or investigations in other grants may be extended to this grant, if:

- (a) the beneficiary concerned is found, in other EU grants awarded under similar conditions, to have committed systemic or recurrent errors, irregularities, fraud or breach of obligations that have a material impact on this grant and
- (b) those findings are formally notified to the beneficiary concerned — together with the list of grants affected by the findings — within the time-limit for audits set out in the Data Sheet (see Point 6).

The granting authority will formally notify the beneficiary concerned of the intention to extend the findings and the list of grants affected.

If the extension concerns **rejections of lump sum contributions**: the notification will include:

- (a) an invitation to submit observations on the list of grants affected by the findings
- (b) the request to submit revised financial statements for all grants affected
- (c) the correction rate for extrapolation, established on the basis of the systemic or recurrent errors, to calculate the amounts to be rejected, if the beneficiary concerned:
 - (i) considers that the submission of revised financial statements is not possible or practicable or
 - (ii) does not submit revised financial statements.

If the extension concerns **grant reductions**: the notification will include:

- (a) an invitation to submit observations on the list of grants affected by the findings and
- (b) the **correction rate for extrapolation**, established on the basis of the systemic or recurrent errors and the principle of proportionality.

The beneficiary concerned has **60 days** from receiving notification to submit observations, revised financial statements or to propose a duly substantiated **alternative correction method/rate**.

On the basis of this, the granting authority will analyse the impact and decide on the implementation (i.e. start rejection or grant reduction procedures, either on the basis of the revised financial statements or the announced/alternative method/rate or a mix of those; see Articles 27 and 28).

25.6 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, lump sum contributions insufficiently substantiated will be ineligible (see Article 6) and will be rejected (see Article 27), and the grant may be reduced (see Article 28).

Such breaches may also lead to other measures described in Chapter 5.

ARTICLE 26 — IMPACT EVALUATIONS

26.1 Impact evaluation

The granting authority may carry out impact evaluations of the action, measured against the objectives and indicators of the EU programme funding the grant.

Such evaluations may be started during implementation of the action and until the time-limit set out in the Data Sheet (see Point 6). They will be formally notified to the coordinator or beneficiaries and will be considered to start on the date of the notification.

If needed, the granting authority may be assisted by independent outside experts.

The coordinator or beneficiaries must provide any information relevant to evaluate the impact of the action, including information in electronic format.

26.2 Consequences of non-compliance

If a beneficiary breaches any of its obligations under this Article, the granting authority may apply the measures described in Chapter 5.

CHAPTER 5 CONSEQUENCES OF NON-COMPLIANCE

SECTION 1 REJECTIONS AND GRANT REDUCTION

ARTICLE 27 — REJECTION OF CONTRIBUTIONS

27.1 Conditions

The granting authority will — at interim payment, final payment or afterwards — reject any lump sum contributions which are ineligible (see Article 6), in particular following checks, reviews, audits or investigations (see Article 25).

The rejection may also be based on the extension of findings from other grants to this grant (see Article 25).

Ineligible lump sum contributions will be rejected.

27.2 Procedure

If the rejection does not lead to a recovery, the granting authority will formally notify the coordinator or beneficiary concerned of the rejection, the amounts and the reasons why. The coordinator or beneficiary concerned may — within 30 days of receiving notification — submit observations if it disagrees with the rejection (payment review procedure).

If the rejection leads to a recovery, the granting authority will follow the contradictory procedure with pre-information letter set out in Article 22.

27.3 Effects

If the granting authority rejects lump sum contributions, it will deduct them from the lump sum contributions declared and then calculate the amount due (and, if needed, make a recovery; see Article 22).

ARTICLE 28 — GRANT REDUCTION

28.1 Conditions

The granting authority may — at beneficiary termination, final payment or afterwards — reduce the grant for a beneficiary, if:

- (a) the beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed:
 - (i) substantial errors, irregularities or fraud or
 - (ii) serious breach of obligations under this Agreement or during its award (including improper implementation of the action, non-compliance with the call conditions, submission of false information, failure to provide required information, breach of ethics or security rules (if applicable), failure to cooperate with checks, reviews, audits and investigations, etc.), or
- (b) the beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed — in other EU grants awarded to it under similar conditions — systemic or recurrent errors, irregularities, fraud or serious breach of obligations that have a material impact on this grant (extension of findings; see Article 25.5).

The amount of the reduction will be calculated for each beneficiary concerned and proportionate to the

seriousness and the duration of the errors, irregularities or fraud or breach of obligations, by applying an individual reduction rate to their accepted EU contribution.

28.2 Procedure

If the grant reduction does not lead to a recovery, the granting authority will formally notify the coordinator or beneficiary concerned of the reduction, the amount to be reduced and the reasons why. The coordinator or beneficiary concerned may — within 30 days of receiving notification — submit observations if it disagrees with the reduction (payment review procedure).

If the grant reduction leads to a recovery, the granting authority will follow the contradictory procedure with pre-information letter set out in Article 22.

28.3 Effects

If the granting authority reduces the grant, it will deduct the reduction and then calculate the amount due (and, if needed, make a recovery; see Article 22).

SECTION 2 SUSPENSION AND TERMINATION

ARTICLE 29 — PAYMENT DEADLINE SUSPENSION

29.1 Conditions

The granting authority may — at any moment — suspend the payment deadline if a payment cannot be processed because:

- (a) the required report (see Article 21) has not been submitted or is not complete or additional information is needed
- (b) there are doubts about the amount to be paid (e.g. ongoing extension procedure, queries about eligibility, need for a grant reduction, etc.) and additional checks, reviews, audits or investigations are necessary, or
- (c) there are other issues affecting the EU financial interests.

29.2 Procedure

The granting authority will formally notify the coordinator of the suspension and the reasons why.

The suspension will **take effect** the day the notification is sent.

If the conditions for suspending the payment deadline are no longer met, the suspension will be **lifted** — and the remaining time to pay (see Data Sheet, Point 4.2) will resume.

If the suspension exceeds two months, the coordinator may request the granting authority to confirm if the suspension will continue.

If the payment deadline has been suspended due to the non-compliance of the report and the revised report is not submitted (or was submitted but is also rejected), the granting authority may also terminate the grant or the participation of the coordinator (see Article 32).

ARTICLE 30 — PAYMENT SUSPENSION

30.1 Conditions

The granting authority may — at any moment — suspend payments, in whole or in part for one or more beneficiaries, if:

- (a) a beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed or is suspected of having committed:
 - (i) substantial errors, irregularities or fraud or
 - (ii) serious breach of obligations under this Agreement or during its award (including improper implementation of the action, non-compliance with the call conditions, submission of false information, failure to provide required information, breach of ethics or security rules (if applicable), failure to cooperate with checks, reviews, audits and investigations, etc.), or
- (b) a beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed — in other EU grants awarded to it under similar conditions — systemic or recurrent errors, irregularities, fraud or serious breach of obligations that have a material impact on this grant (extension of findings; see Article 25.5).

If payments are suspended for one or more beneficiaries, the granting authority will make partial payment(s) for the part(s) not suspended. If suspension concerns the final payment, the payment (or recovery) of the remaining amount after suspension is lifted will be considered to be the payment that closes the action.

30.2 Procedure

Before suspending payments, the granting authority will send a **pre-information letter** to the beneficiary concerned:

- formally notifying the intention to suspend payments and the reasons why and
- requesting observations within 30 days of receiving notification.

If the granting authority does not receive observations or decides to pursue the procedure despite the observations it has received, it will confirm the suspension (**confirmation letter**). Otherwise, it will formally notify that the procedure is discontinued.

At the end of the suspension procedure, the granting authority will also inform the coordinator.

The suspension will **take effect** the day after the confirmation notification is sent.

If the conditions for resuming payments are met, the suspension will be **lifted**. The granting authority will formally notify the beneficiary concerned (and the coordinator) and set the suspension end date.

During the suspension, no prefinancing will be paid to the beneficiaries concerned. For interim payments, the periodic reports for all reporting periods except the last one (see Article 21) must

not contain any financial statements from the beneficiary concerned (or its affiliated entities). The coordinator must include them in the next periodic report after the suspension is lifted or — if suspension is not lifted before the end of the action — in the last periodic report.

ARTICLE 31 — GRANT AGREEMENT SUSPENSION

31.1 Consortium-requested GA suspension

31.1.1 Conditions and procedure

The beneficiaries may request the suspension of the grant or any part of it, if exceptional circumstances — in particular *force majeure* (see Article 35) — make implementation impossible or excessively difficult.

The coordinator must submit a request for **amendment** (see Article 39), with:

- the reasons why
- the date the suspension takes effect; this date may be before the date of the submission of the amendment request and
- the expected date of resumption.

The suspension will **take effect** on the day specified in the amendment.

Once circumstances allow for implementation to resume, the coordinator must immediately request another **amendment** of the Agreement to set the suspension end date, the resumption date (one day after suspension end date), extend the duration and make other changes necessary to adapt the action to the new situation (see Article 39) — unless the grant has been terminated (see Article 32). The suspension will be **lifted** with effect from the suspension end date set out in the amendment. This date may be before the date of the submission of the amendment request.

During the suspension, no prefinancing will be paid. Moreover, no work may be done. Ongoing work packages must be interrupted and no new work packages may be started.

31.2 EU-initiated GA suspension

31.2.1 Conditions

The granting authority may suspend the grant or any part of it, if:

- (a) a beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed or is suspected of having committed:
 - (i) substantial errors, irregularities or fraud or
 - (ii) serious breach of obligations under this Agreement or during its award (including improper implementation of the action, non-compliance with the call conditions, submission of false information, failure to provide required information, breach of ethics or security rules (if applicable), failure to cooperate with checks, reviews, audits and investigations, etc.), or

(b) a beneficiary (or a person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed — in other EU grants awarded to it under similar conditions — systemic or recurrent errors, irregularities, fraud or serious breach of obligations that have a material impact on this grant (extension of findings; see Article 25.5)

(c) other:

(i) linked action issues: not applicable

(ii) due to major delays, the objectives of the action risk to no longer be achieved

31.2.2 Procedure

Before suspending the grant, the granting authority will send a **pre-information letter** to the coordinator:

- formally notifying the intention to suspend the grant and the reasons why and
- requesting observations within 30 days of receiving notification.

If the granting authority does not receive observations or decides to pursue the procedure despite the observations it has received, it will confirm the suspension (**confirmation letter**). Otherwise, it will formally notify that the procedure is discontinued.

The suspension will **take effect** the day after the confirmation notification is sent (or on a later date specified in the notification).

Once the conditions for resuming implementation of the action are met, the granting authority will formally notify the coordinator a **lifting of suspension letter**, in which it will set the suspension end date and invite the coordinator to request an amendment of the Agreement to set the resumption date (one day after suspension end date), extend the duration and make other changes necessary to adapt the action to the new situation (see Article 39) — unless the grant has been terminated (see Article 32). The suspension will be **lifted** with effect from the suspension end date set out in the lifting of suspension letter. This date may be before the date on which the letter is sent.

During the suspension, no prefinancing will be paid. Moreover, no work may be done. Ongoing work packages must be interrupted and no new work packages may be started.

The beneficiaries may not claim damages due to suspension by the granting authority (see Article 33).

Grant suspension does not affect the granting authority's right to terminate the grant or a beneficiary (see Article 32) or reduce the grant (see Article 28).

ARTICLE 32 — GRANT AGREEMENT OR BENEFICIARY TERMINATION

32.1 Consortium-requested GA termination

32.1.1 Conditions and procedure

The beneficiaries may request the termination of the grant.

The coordinator must submit a request for **amendment** (see Article 39), with:

- the reasons why
- the date the consortium ends work on the action ('end of work date') and
- the date the termination takes effect ('termination date'); this date must be after the date of the submission of the amendment request.

The termination will **take effect** on the termination date specified in the amendment.

If no reasons are given or if the granting authority considers the reasons do not justify termination, it may consider the grant terminated improperly.

32.1.2 Effects

The coordinator must — within 60 days from when termination takes effect — submit a **periodic report** (for the open reporting period until termination).

The granting authority will calculate the final grant amount and final payment on the basis of the report submitted and taking into account the lump sum contributions for activities implemented before the end of work date (see Article 22). Partial lump sum contributions for work packages that were not completed (e.g. due to technical reasons) may exceptionally be taken into account.

If the granting authority does not receive the report within the deadline, only lump sum contributions which are included in an approved periodic report will be taken into account (no contributions if no periodic report was ever approved).

Improper termination may lead to a grant reduction (see Article 28).

After termination, the beneficiaries' obligations (in particular Articles 13 (confidentiality and security), 16 (IPR), 17 (communication, dissemination and visibility), 21 (reporting), 25 (checks, reviews, audits and investigations), 26 (impact evaluation), 27 (rejections), 28 (grant reduction) and 42 (assignment of claims)) continue to apply.

32.2 Consortium-requested beneficiary termination

32.2.1 Conditions and procedure

The coordinator may request the termination of the participation of one or more beneficiaries, on request of the beneficiary concerned or on behalf of the other beneficiaries.

The coordinator must submit a request for **amendment** (see Article 39), with:

- the reasons why
- the opinion of the beneficiary concerned (or proof that this opinion has been requested in writing)
- the date the beneficiary ends work on the action ('end of work date')
- the date the termination takes effect ('termination date'); this date must be after the date of the submission of the amendment request.

If the termination concerns the coordinator and is done without its agreement, the amendment request must be submitted by another beneficiary (acting on behalf of the consortium).

The termination will **take effect** on the termination date specified in the amendment.

If no information is given or if the granting authority considers that the reasons do not justify termination, it may consider the beneficiary to have been terminated improperly.

32.2.2 Effects

The coordinator must — within 60 days from when termination takes effect — submit:

- (i) a **report on the distribution of payments** to the beneficiary concerned
- (ii) a **termination report** from the beneficiary concerned, for the open reporting period until termination, containing an overview of the progress of the work
- (iii) a second **request for amendment** (see Article 39) with other amendments needed (e.g. reallocation of the tasks and the estimated budget of the terminated beneficiary; addition of a new beneficiary to replace the terminated beneficiary; change of coordinator, etc.).

The granting authority will calculate the amount due to the beneficiary on the basis of the reports submitted in previous interim payments (i.e. beneficiary's lump sum contributions for completed and approved work packages).

Lump sum contributions for ongoing/not yet completed work packages will have to be included in the periodic report for the next reporting periods when those work packages have been completed.

If the granting authority does not receive the report on the distribution of payments within the deadline, it will consider that:

- the coordinator did not distribute any payment to the beneficiary concerned and that
- the beneficiary concerned must not repay any amount to the coordinator.

If the second request for amendment is accepted by the granting authority, the Agreement is **amended** to introduce the necessary changes (see Article 39).

If the second request for amendment is rejected by the granting authority (because it calls into question the decision awarding the grant or breaches the principle of equal treatment of applicants), the grant may be terminated (see Article 32).

Improper termination may lead to a reduction of the grant (see Article 31) or grant termination (see Article 32).

After termination, the concerned beneficiary's obligations (in particular Articles 13 (confidentiality and security), 16 (IPR), 17 (communication, dissemination and visibility), 21 (reporting), 25 (checks, reviews, audits and investigations), 26 (impact evaluation), 27 (rejections), 28 (grant reduction) and 42 (assignment of claims)) continue to apply.

32.3 EU-initiated GA or beneficiary termination

32.3.1 Conditions

The granting authority may terminate the grant or the participation of one or more beneficiaries, if:

- (a) one or more beneficiaries do not accede to the Agreement (see Article 40)
- (b) a change to the action or the legal, financial, technical, organisational or ownership situation of a beneficiary is likely to substantially affect the implementation of the action or calls into question the decision to award the grant (including changes linked to one of the exclusion grounds listed in the declaration of honour)
- (c) following termination of one or more beneficiaries, the necessary changes to the Agreement (and their impact on the action) would call into question the decision awarding the grant or breach the principle of equal treatment of applicants
- (d) implementation of the action has become impossible or the changes necessary for its continuation would call into question the decision awarding the grant or breach the principle of equal treatment of applicants
- (e) a beneficiary (or person with unlimited liability for its debts) is subject to bankruptcy proceedings or similar (including insolvency, winding-up, administration by a liquidator or court, arrangement with creditors, suspension of business activities, etc.)
- (f) a beneficiary (or person with unlimited liability for its debts) is in breach of social security or tax obligations
- (g) a beneficiary (or person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has been found guilty of grave professional misconduct
- (h) a beneficiary (or person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed fraud, corruption, or is involved in a criminal organisation, money laundering, terrorism-related crimes (including terrorism financing), child labour or human trafficking
- (i) a beneficiary (or person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) was created under a different jurisdiction with the intent to circumvent fiscal, social or other legal obligations in the country of origin (or created another entity with this purpose)
- (j) a beneficiary (or person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed:
 - (i) substantial errors, irregularities or fraud or
 - (ii) serious breach of obligations under this Agreement or during its award (including improper implementation of the action, non-compliance with the call conditions, submission of false information, failure to provide required information, breach of ethics or security rules (if applicable), failure to cooperate with checks, reviews, audits and investigations, etc.)
- (k) a beneficiary (or person having powers of representation, decision-making or control, or person essential for the award/implementation of the grant) has committed — in other EU grants awarded to it under similar conditions — systemic or recurrent errors, irregularities, fraud or

serious breach of obligations that have a material impact on this grant (extension of findings; see Article 25.5)

- (l) despite a specific request by the granting authority, a beneficiary does not request — through the coordinator — an amendment to the Agreement to end the participation of one of its affiliated entities or associated partners that is in one of the situations under points (d), (f), (e), (g), (h), (i) or (j) and to reallocate its tasks, or
- (m) other:
 - (i) linked action issues: not applicable
 - (ii) due to major delays, the objectives of the action can no longer be achieved

32.3.2 Procedure

Before terminating the grant or participation of one or more beneficiaries, the granting authority will send a **pre-information letter** to the coordinator or beneficiary concerned:

- formally notifying the intention to terminate and the reasons why and
- requesting observations within 30 days of receiving notification.

If the granting authority does not receive observations or decides to pursue the procedure despite the observations it has received, it will confirm the termination and the date it will take effect (**confirmation letter**). Otherwise, it will formally notify that the procedure is discontinued.

For beneficiary terminations, the granting authority will — at the end of the procedure — also inform the coordinator.

The termination will **take effect** the day after the confirmation notification is sent (or on a later date specified in the notification; ‘termination date’).

32.3.3 Effects

- (a) for **GA termination**:

The coordinator must — within 60 days from when termination takes effect — submit a **periodic report** (for the last open reporting period until termination).

The granting authority will calculate the final grant amount and final payment on the basis of the report submitted and taking into account the lump sum contributions for activities implemented before termination takes effect (see Article 22). Partial lump sum contributions for work packages that were not completed (e.g. due to technical reasons) may exceptionally be taken into account.

If the grant is terminated for breach of the obligation to submit reports, the coordinator may not submit any report after termination.

If the granting authority does not receive the report within the deadline, only lump sum contributions which are included in an approved periodic report will be taken into account (no contributions if no periodic report was ever approved).

Termination does not affect the granting authority's right to reduce the grant (see Article 28) or to impose administrative sanctions (see Article 34).

The beneficiaries may not claim damages due to termination by the granting authority (see Article 33).

After termination, the beneficiaries' obligations (in particular Articles 13 (confidentiality and security), 16 (IPR), 17 (communication, dissemination and visibility), 21 (reporting), 25 (checks, reviews, audits and investigations), 26 (impact evaluation), 27 (rejections), 28 (grant reduction) and 42 (assignment of claims)) continue to apply.

(b) for **beneficiary termination**:

The coordinator must — within 60 days from when termination takes effect — submit:

- (i) a **report on the distribution of payments** to the beneficiary concerned
- (ii) a **termination report** from the beneficiary concerned, for the open reporting period until termination, containing an overview of the progress of the work
- (iii) a **request for amendment** (see Article 39) with any amendments needed (e.g. reallocation of the tasks and the estimated budget of the terminated beneficiary; addition of a new beneficiary to replace the terminated beneficiary; change of coordinator, etc.).

The granting authority will calculate the amount due to the beneficiary on the basis of the reports submitted in previous interim payments (i.e. beneficiary's lump sum contributions for completed and approved work packages).

Lump sum contributions for ongoing/not yet completed work packages will have to be included in the periodic report for the next reporting periods when those work packages have been completed.

If the granting authority does not receive the report on the distribution of payments within the deadline, it will consider that:

- the coordinator did not distribute any payment to the beneficiary concerned and that
- the beneficiary concerned must not repay any amount to the coordinator.

If the request for amendment is accepted by the granting authority, the Agreement is **amended** to introduce the necessary changes (see Article 39).

If the request for amendment is rejected by the granting authority (because it calls into question the decision awarding the grant or breaches the principle of equal treatment of applicants), the grant may be terminated (see Article 32).

After termination, the concerned beneficiary's obligations (in particular Articles 13 (confidentiality and security), 16 (IPR), 17 (communication, dissemination and visibility), 21 (reporting), 25 (checks, reviews, audits and investigations), 26 (impact evaluation), 27 (rejections), 28 (grant reduction) and 42 (assignment of claims)) continue to apply.

SECTION 3 OTHER CONSEQUENCES: DAMAGES AND ADMINISTRATIVE SANCTIONS

ARTICLE 33 — DAMAGES

33.1 Liability of the granting authority

The granting authority cannot be held liable for any damage caused to the beneficiaries or to third parties as a consequence of the implementation of the Agreement, including for gross negligence.

The granting authority cannot be held liable for any damage caused by any of the beneficiaries or other participants involved in the action, as a consequence of the implementation of the Agreement.

33.2 Liability of the beneficiaries

The beneficiaries must compensate the granting authority for any damage it sustains as a result of the implementation of the action or because the action was not implemented in full compliance with the Agreement, provided that it was caused by gross negligence or wilful act.

The liability does not extend to indirect or consequential losses or similar damage (such as loss of profit, loss of revenue or loss of contracts), provided such damage was not caused by wilful act or by a breach of confidentiality.

ARTICLE 34 — ADMINISTRATIVE SANCTIONS AND OTHER MEASURES

Nothing in this Agreement may be construed as preventing the adoption of administrative sanctions (i.e. exclusion from EU award procedures and/or financial penalties) or other public law measures, in addition or as an alternative to the contractual measures provided under this Agreement (see, for instance, Articles 137 to 148 EU Financial Regulation 2024/2509 and Articles 4 and 7 of Regulation 2988/95²⁰).

SECTION 4 FORCE MAJEURE

ARTICLE 35 — FORCE MAJEURE

A party prevented by force majeure from fulfilling its obligations under the Agreement cannot be considered in breach of them.

‘Force majeure’ means any situation or event that:

- prevents either party from fulfilling their obligations under the Agreement
- was unforeseeable, exceptional situation and beyond the parties’ control
- was not due to error or negligence on their part (or on the part of other participants involved in the action) and
- proves to be inevitable in spite of exercising all due diligence.

²⁰ Council Regulation (EC, Euratom) No 2988/95 of 18 December 1995 on the protection of the European Communities financial interests (OJ L 312, 23.12.1995, p. 1).

Any situation constituting force majeure must be formally notified to the other party without delay, stating the nature, likely duration and foreseeable effects.

The parties must immediately take all the necessary steps to limit any damage due to force majeure and do their best to resume implementation of the action as soon as possible.

CHAPTER 6 FINAL PROVISIONS

ARTICLE 36 — COMMUNICATION BETWEEN THE PARTIES

36.1 Forms and means of communication — Electronic management

EU grants are managed fully electronically through the EU Funding & Tenders Portal ('Portal').

All communications must be made electronically through the Portal in accordance with the Portal Terms and Conditions and using the forms and templates provided there (except if explicitly instructed otherwise by the granting authority).

Communications must be made in writing and clearly identify the grant agreement (project number and acronym).

Communications must be made by persons authorised according to the Portal Terms and Conditions. For naming the authorised persons, each beneficiary must have designated — before the signature of this Agreement — a 'legal entity appointed representative (LEAR)'. The role and tasks of the LEAR are stipulated in their appointment letter (see Portal Terms and Conditions).

If the electronic exchange system is temporarily unavailable, instructions will be given on the Portal.

36.2 Date of communication

The sending date for communications made through the Portal will be the date and time of sending, as indicated by the time logs.

The receiving date for communications made through the Portal will be the date and time the communication is accessed, as indicated by the time logs. Formal notifications that have not been accessed within 10 days after sending, will be considered to have been accessed (see Portal Terms and Conditions).

If a communication is exceptionally made on paper (by e-mail or postal service), general principles apply (i.e. date of sending/receipt). Formal notifications by registered post with proof of delivery will be considered to have been received either on the delivery date registered by the postal service or the deadline for collection at the post office.

If the electronic exchange system is temporarily unavailable, the sending party cannot be considered in breach of its obligation to send a communication within a specified deadline.

36.3 Addresses for communication

The Portal can be accessed via the Europa website.

The address for paper communications to the granting authority (if exceptionally allowed) is the official mailing address indicated on its website.

For beneficiaries, it is the legal address specified in the Portal Participant Register.

ARTICLE 37 — INTERPRETATION OF THE AGREEMENT

The provisions in the Data Sheet take precedence over the rest of the Terms and Conditions of the Agreement.

Annex 5 takes precedence over the Terms and Conditions.

The Terms and Conditions take precedence over the Annexes other than Annex 5.

Annex 2 takes precedence over Annex 1.

ARTICLE 38 — CALCULATION OF PERIODS AND DEADLINES

In accordance with Regulation No 1182/71²¹, periods expressed in days, months or years are calculated from the moment the triggering event occurs.

The day during which that event occurs is not considered as falling within the period.

‘Days’ means calendar days, not working days.

ARTICLE 39 — AMENDMENTS

39.1 Conditions

The Agreement may be amended, unless the amendment entails changes to the Agreement which would call into question the decision awarding the grant or breach the principle of equal treatment of applicants.

Amendments may be requested by any of the parties.

39.2 Procedure

The party requesting an amendment must submit a request for amendment signed directly in the Portal Amendment tool.

The coordinator submits and receives requests for amendment on behalf of the beneficiaries (see Annex 3). If a change of coordinator is requested without its agreement, the submission must be done by another beneficiary (acting on behalf of the other beneficiaries).

The request for amendment must include:

- the reasons why
- the appropriate supporting documents and

²¹ Regulation (EEC, Euratom) No 1182/71 of the Council of 3 June 1971 determining the rules applicable to periods, dates and time-limits (OJ L 124, 8/6/1971, p. 1).

- for a change of coordinator without its agreement: the opinion of the coordinator (or proof that this opinion has been requested in writing).

The granting authority may request additional information.

If the party receiving the request agrees, it must sign the amendment in the tool within 45 days of receiving notification (or any additional information the granting authority has requested). If it does not agree, it must formally notify its disagreement within the same deadline. The deadline may be extended, if necessary for the assessment of the request. If no notification is received within the deadline, the request is considered to have been rejected.

An amendment **enters into force** on the day of the signature of the receiving party.

An amendment **takes effect** on the date of entry into force or other date specified in the amendment.

ARTICLE 40 — ACCESSION AND ADDITION OF NEW BENEFICIARIES

40.1 Accession of the beneficiaries mentioned in the Preamble

The beneficiaries which are not coordinator must accede to the grant by signing the accession form (see Annex 3) directly in the Portal Grant Preparation tool, within 30 days after the entry into force of the Agreement (see Article 44).

They will assume the rights and obligations under the Agreement with effect from the date of its entry into force (see Article 44).

If a beneficiary does not accede to the grant within the above deadline, the coordinator must — within 30 days — request an amendment (see Article 39) to terminate the beneficiary and make any changes necessary to ensure proper implementation of the action. This does not affect the granting authority's right to terminate the grant (see Article 32).

40.2 Addition of new beneficiaries

In justified cases, the beneficiaries may request the addition of a new beneficiary.

For this purpose, the coordinator must submit a request for amendment in accordance with Article 39. It must include an accession form (see Annex 3) signed by the new beneficiary directly in the Portal Amendment tool.

New beneficiaries will assume the rights and obligations under the Agreement with effect from the date of their accession specified in the accession form (see Annex 3).

Additions are also possible in mono-beneficiary grants.

ARTICLE 41 — TRANSFER OF THE AGREEMENT

In justified cases, the beneficiary of a mono-beneficiary grant may request the transfer of the grant to a new beneficiary, provided that this would not call into question the decision awarding the grant or breach the principle of equal treatment of applicants.

The beneficiary must submit a request for **amendment** (see Article 39), with

- the reasons why
- the accession form (see Annex 3) signed by the new beneficiary directly in the Portal Amendment tool and
- additional supporting documents (if required by the granting authority).

The new beneficiary will assume the rights and obligations under the Agreement with effect from the date of accession specified in the accession form (see Annex 3).

ARTICLE 42 — ASSIGNMENTS OF CLAIMS FOR PAYMENT AGAINST THE GRANTING AUTHORITY

The beneficiaries may not assign any of their claims for payment against the granting authority to any third party, except if expressly approved in writing by the granting authority on the basis of a reasoned, written request by the coordinator (on behalf of the beneficiary concerned).

If the granting authority has not accepted the assignment or if the terms of it are not observed, the assignment will have no effect on it.

In no circumstances will an assignment release the beneficiaries from their obligations towards the granting authority.

ARTICLE 43 — APPLICABLE LAW AND SETTLEMENT OF DISPUTES

43.1 Applicable law

The Agreement is governed by the applicable EU law, supplemented if necessary by the law of Belgium.

Special rules may apply for beneficiaries which are international organisations (if any; see Data Sheet, Point 5).

43.2 Dispute settlement

If a dispute concerns the interpretation, application or validity of the Agreement, the parties must bring action before the EU General Court — or, on appeal, the EU Court of Justice — under Article 272 of the Treaty on the Functioning of the EU (TFEU).

For non-EU beneficiaries (if any), such disputes must be brought before the courts of Brussels, Belgium — unless an international agreement provides for the enforceability of EU court judgements.

For beneficiaries with arbitration as special dispute settlement forum (if any; see Data Sheet, Point 5), the dispute will — in the absence of an amicable settlement — be settled in accordance with the Rules for Arbitration published on the Portal.

If a dispute concerns administrative sanctions, offsetting or an enforceable decision under Article 299 TFEU (see Articles 22 and 34), the beneficiaries must bring action before the General Court — or, on appeal, the Court of Justice — under Article 263 TFEU.

For grants where the granting authority is an EU executive agency (see Preamble), actions against

offsetting and enforceable decisions must be brought against the European Commission (not against the granting authority; see also Article 22).

ARTICLE 44 — ENTRY INTO FORCE

The Agreement will enter into force on the day of signature by the granting authority or the coordinator, depending on which is later.

SIGNATURES

For the coordinator

For the granting authority



ANNEX 1



Just Transition Mechanism (JTM)

Description of the action (DoA)

Part A

Part B

DESCRIPTION OF THE ACTION (PART A)

COVER PAGE

Part A of the Description of the Action (DoA) must be completed directly on the Portal Grant Preparation screens.

PROJECT	
Grant Preparation (General Information screen) — Enter the info.	
Project number:	101192431
Project name:	Affordable student housing for the University of Ostrava
Project acronym:	2024-6-CZ-Dormitory
Call:	JTM-2022-2025-PSLF
Topic:	JTM-2022-2025-PSLF-STANDALONE-PROJECTS
Type of action:	JTM-LS
Service:	CINEA/B/02
Project starting date:	fixed date: 12 June 2025
Project duration:	24 months

TABLE OF CONTENTS

Project summary3

List of participants 3

List of work packages4

Staff effort 8

List of deliverables9

List of milestones (outputs/outcomes) 11

List of critical risks 12

PROJECT SUMMARY

Project summary

Grant Preparation (General Information screen) — Provide an overall description of your project (including context and overall objectives, planned activities and main achievements, and expected results and impacts (on target groups, change procedures, capacities, innovation etc)). This summary should give readers a clear idea of what your project is about.

Use the project summary from your proposal.

The University of Ostrava (OU) in Czechia aims to build a new dormitory (block C) with a housing capacity of 332 beds next to the existing blocks A and B, mainly for students from other Czech regions and countries who represent one-third of the OU students.

The project's goal is to expand the affordable student housing in the Moravian-Silesian Region, a coal region undergoing transition to a low-carbon economy. The project will address the population decline and labour market mismatch by providing social infrastructure for education and housing. It will help to prevent the youth from leaving, attract more students from other regions and abroad, and improve the local labour market, thus indirectly supporting the diversification of the local economy.

The project will also contribute to sustainability by applying a building design that integrates the use of renewable energy sources and smart solutions. The new building will have low energy and water consumption as it will use geothermal heat pumps, solar panels, dichroic façade and high-quality insulation for thermoregulation, and water harvesting system. The expected energy performance score of the new building is EPC B.

The project is supported by an EU grant (EUR 1.303 million) under PSLF, complemented by a loan (EUR 5.214 million) awarded by the EIB via the National Development Bank, and other national grants (EUR 12.105 million), bringing the total project budget to EUR 18.622 million.

LIST OF PARTICIPANTS

PARTICIPANTS

Grant Preparation (Beneficiaries screen) — Enter the info.

Number	Role	Short name	Legal name	Country	PIC
1	COO	OU	OSTRAVSKA UNIVERZITA	CZ	998738870

LIST OF WORK PACKAGES

Work packages						
Grant Preparation (Work Packages screen) — Enter the info.						
Work Package No	Work Package name	Lead Beneficiary	Effort (Person-Months)	Start Month	End Month	Deliverables
WP1	Project management and communication	1 - OU	0.00	1	24	D1.1 – Progress report 1 D1.2 – Communication Plan
WP2	Construction of the new dormitory	1 - OU	0.00	1	24	D2.1 – Certificate of completion of works for the new dormitory

Work package WP1 – Project management and communication

Work Package Number	WP1	Lead Beneficiary	1 - OU
Work Package Name	Project management and communication		
Start Month	1	End Month	24

Objectives

The objective of WP1 is to implement the project management, coordination, monitoring, reporting, and communication activities and ensure compliance of all project activities with the objectives set forward in the Grant Agreement.

Description**ACTIVITIES**

This WP includes all activities related to project management, coordination, monitoring, reporting, and communication, including:

- Project management activities (legal, contractual, financial, and administrative management)
- Monitoring activities (meetings, coordination, project monitoring and evaluation, progress reports, etc.)
- Coordination of project tasks at the management, operational and implementation levels
- Continuous risk assessment and mitigation
- Quality assessment of project outputs
- Coordination with CINEA
- Communication activities
- Any other cross-cutting activities

TASKS

The following tasks will be carried out by OU:

- Preparation of the annual progress report and final periodic report required by CINEA and other supporting documents, including regular update of the SyGMA continuous reporting module
- Continuous monitoring of the project's technical and financial progress
- Organisation of regular meetings between the various project stakeholders (senior management, construction manager, project manager, financial manager, legal manager, etc.)
- Assessment of the project risks and on-the-spot problem-solving
- Preparation of a Communication Plan
- Development of a project communication toolkit, consisting of website publications, social media presence, printing of roll-up banners and billboards, preparation of reports and presentations, etc.
- Promotion of project results via website, social media, newsletters, etc.
- Organisation of events promoting the project results, including an inauguration ceremony

EXPECTED RESULTS

- Efficient, transparent, and sound administrative and financial coordination of the project
- Continuous monitoring of project progress, including the delivery of high-quality outputs
- Timely identification of project risks and implementation of mitigation measures and contingency plans
- Timely delivery of project results
- Promotion of the project and of the received EU funding

Work package WP2 – Construction of the new dormitory

Work Package Number	WP2	Lead Beneficiary	1 - OU
Work Package Name	Construction of the new dormitory		
Start Month	1	End Month	24

Objectives

The objective of WP2 is the construction of a new Ostrava University dormitory (block C) next to the existing dormitories

(blocks A and B), with the total housing capacity of approx. 165 rooms, including 4 double rooms for 8 persons with special needs and 6 rooms suitable for families with children, for approx. 332 students in total.

Description

ACTIVITIES

This WP relates to the construction of a new 5-storey dormitory with approx. 165 rooms located in Ostrava through the following activities:

- Site preparation works,
- Construction works for a 5-storey building with approx. 165 rooms carried out by a contractor and supervised by OU and any additional elements such as bike shelters, special accessibility measures, if necessary,
- Construction of technical rooms designed to accommodate and distribute utilities such as electricity, water, heating, and fiber,
- Construction of parking areas and roadways for vehicles, bicycles, and pedestrians,
- Technical and safety supervision, acquisition, delivery and installation of active network elements including accessories and interior equipment (furniture, appliances, etc.).

The construction works and supervision as well as the installation of active network elements including accessories and furniture and appliances will be carried out by the selected contractors.

TASKS

The following tasks will be carried out by the OU and the selected contractors:

The OU's tasks include:

- Signature of the contracts with the selected contractors,
- Handover of the construction site to the construction contractor to start the construction works,
- Supervision of the construction works and compliance with the technical and safety standards,
- Acceptance of the handover of the completed construction works,
- Acceptance of the handover of the delivered and installed active network elements and furniture,
- Preparation of a detailed final report on the implementation of the works, including an evaluation of the implementation process.

The tasks of the contractor for construction works include:

- Demolition of the existing building,
- Site preparation works:
 - Excavation works for building foundation,
 - Excavation of geothermal wells,
 - Creation of parking areas,
 - Development of the outdoor environment,
 - Sorting out construction and demolition waste.
- Construction of a 5-storey dormitory with approx. 332 places (beds) and an area of approx. 3000 m² of interior surface:
 - Construction of approx. 152 underground parking spaces,
 - Installation of 2 elevators,
 - Construction of a technical room designed to accommodate and distribute utilities,
 - Installation of approx. 62 geothermal wells, 2 heat pumps with the total energy output of 444 kW, approx. 147 solar panels with the energy output of 225 kWp, 3305 m² of dichroic façade and 171 m² of glass windows. The heating system will be based on geothermal technology using groundwater heat pump,
 - Technical installations for increased safety (ventilation with sensors, smoke detectors, fire blankets),
 - Finishing works (electrotechnical installations, interior work, technical equipment, built-in furniture, etc.),
 - Installation of technical solutions for ensuring the accessibility of the building and outdoor areas: paved access areas supplemented with guidelines and warning strips; floors connected by elevators; barrier-free sidewalks; wheelchair-accessible ramps, entrances, seating and resting areas, etc.
- Grid/media connection to the building (municipal water, waste management, fiber/internet, electricity),
- Road interventions,
- Establishment of a waste sorting area,
- Approval by the building authority,
- Handover of the building to the beneficiary.

The tasks of the contractor for construction supervision include:

- Inspecting construction works,
- Checking technical compliance of the construction works with the standards set out in the design documentation,
- Checking compliance of the construction works with the national safety and health standards,

- Ensuring high-quality and timely execution of the construction works.

The tasks of the contractor for the active network elements including accessories (e.g. switches, routers, Wi-Fi active elements) supply include:

- Delivery and installation of active network elements including accessories for the block C
- Connecting the building to the digital utility network, including one server room.

The tasks of the contractor for the furniture, interior equipment and appliances supply include:

- Interior furnishing, including installation of technical appliances, of approx. 165 rooms,
- Interior furnishing of 3 staff offices,
- Installation of other furniture and equipment for the reception, common area, halls, 4 study rooms, 6 kitchens, laundry room, gym (fitness equipment), etc.

EXPECTED RESULTS

The following results are expected:

- A new 5-storey accessible student dormitory with a total area of approximately 3,000 m² built, providing fully equipped and furnished accommodation for about 332 students, including around 165 rooms, among them 4 double rooms (for 8 persons) designed for students with special needs and 6 rooms suitable for families with children.
- Parking spaces for approx. 152 cars built.
- A technical room built.
- 2 elevators installed.
- Technical interventions for increased safety conducted.
- An energy-efficient heating system installed.
- Roadways for vehicles, bicycles and pedestrians built.
- Technical and safety supervision conducted throughout the project implementation.
- Active network elements equipment and furniture delivered and installed.

EXPECTED BENEFITS

The following benefits are expected:

- A building with a high energy performance level (expected energy performance score B),
- Gender-neutral housing and education facilities for students.
- New jobs created – Total number = 7 (FTE): Male 2, Female 5.
- Persons reached / direct beneficiaries of the project (students living in dormitory and tourists staying in dormitory) – approx. 4 980 persons within the project's economic life of 17 years.

STAFF EFFORT

Staff effort per participant <i>Grant Preparation (Work packages - Effort screen) — Enter the info.</i>			
Participant	WP1	WP2	Total Person-Months
Total Person-Months	0.00	0.00	0.00

LIST OF DELIVERABLES

Deliverables Grant Preparation (Deliverables screen) — Enter the info. The labels used mean: Public — fully open ( automatically posted online) Sensitive — limited under the conditions of the Grant Agreement EU classified —RESTREINT-UE/EU-RESTRICTED, CONFIDENTIEL-UE/EU-CONFIDENTIAL, SECRET-UE/EU-SECRET under Decision 2015/444						
Deliverable No	Deliverable Name	Work Package No	Lead Beneficiary	Type	Dissemination Level	Due Date (month)
D1.1	Progress report 1	WP1	1 - OU	R — Document, report	PU - Public	13
D1.2	Communication Plan	WP1	1 - OU	R — Document, report	PU - Public	9
D2.1	Certificate of completion of works for the new dormitory	WP2	1 - OU	R — Document, report	SEN - Sensitive	24

Deliverable D1.1 – Progress report 1

Deliverable Number	D1.1	Lead Beneficiary	1 - OU
Deliverable Name	Progress report 1		
Type	R — Document, report	Dissemination Level	PU - Public
Due Date (month)	13	Work Package No	WP1

Description
The progress report will detail the actual progress of the project per WP for the period from month 1 until month 12. It will also refer to the main implementation issues, milestones, events, or factors that affected the progress of the project. Finally, it will include the planned progress per WP until the end of the project. The progress report will be submitted in the PSLF template available on the Funding & Tenders Portal.

Deliverable D1.2 – Communication Plan

Deliverable Number	D1.2	Lead Beneficiary	1 - OU
Deliverable Name	Communication Plan		
Type	R — Document, report	Dissemination Level	PU - Public
Due Date (month)	9	Work Package No	WP1

Description
The communication plan will aim at raising awareness of the project (the new construction) and promoting its outcomes by providing targeted information to multiple audiences, including the media and the public. The communication activities will ensure the visibility of the project as well as acknowledge the EU support in line with the applicable rules for the visibility of the EU funding. The activities will include publication of information on website and press releases, acknowledgement of EU funding received, installation of billboards/commemorative plaque, organisation of a ceremony at the start/end of construction works complemented with a press conference for the local press, publication of a press release at the start/end of construction, etc.

Deliverable D2.1 – Certificate of completion of works for the new dormitory

Deliverable Number	D2.1	Lead Beneficiary	1 - OU
Deliverable Name	Certificate of completion of works for the new dormitory		
Type	R — Document, report	Dissemination Level	SEN - Sensitive
Due Date (month)	24	Work Package No	WP2

Description
Certificate(s) from the selected construction contractor confirming the completion of works and the compliance with the technical specifications set in the works contract, including the acceptance report signed by OU.
The Certificate(s) will confirm that the following results were reached: • A new dormitory with the total housing capacity of approx. 165 rooms, including 4 double rooms for 8 persons with special needs and 6 rooms suitable for families with children, built.

LIST OF MILESTONES

Milestones <i>Grant Preparation (Milestones screen) — Enter the info.</i>					
Milestone No	Milestone Name	Work Package No	Lead Beneficiary	Means of Verification	Due Date (month)
1	Publication of a press release announcing the start of the works	WP1	1 - OU	Published press release (link)	1
2	Start of construction works	WP2	1 - OU	Contractor's acceptance to start the construction works signed by the beneficiary and the contractor (copy)	1
3	End of construction works	WP2	1 - OU	Certificate of completion of works and compliance with technical specifications by the contractor (copy). Works acceptance report signed by the local building authorities (copy)	24
4	Start of construction supervision	WP2	1 - OU	Contractor's acceptance to start the construction supervision signed by the beneficiary and the construction manager (copy)	1
5	End of construction supervision	WP2	1 - OU	Report on the removal of the last defects and incompleteness identified upon completion and handover of the completed construction [according to the construction management contract] (copy)	24
6	Delivery and installation of active network elements and furniture	WP2	1 - OU	Certificate of acceptance of delivery and installation of active network elements and furniture (copy)	24
7	Publication of a press release announcing the end of the works	WP1	1 - OU	Published press release (link)	24

LIST OF CRITICAL RISKS

Critical risks & risk management strategy			
Grant Preparation (Critical Risks screen) — Enter the info.			
Risk number	Description	Work Package No(s)	Proposed Mitigation Measures
1	Unplanned additional construction costs threatening the execution of the project's financial plan Impact – high Likelihood – medium	WP2	• Preparing high-quality project documentation, including all necessary studies and surveys • Ensuring high-quality technical supervision of the construction works • Relying on the experience with the previous construction projects • Creating a financial reserve to cover any additional costs
2	Significant increase of the expected operating costs Impact – medium Likelihood – medium	WP1	• Including a reserve amount for additional operating costs in the financial plan. The reserve amount will be based on an analysis of the existing costs complemented by the expected operating costs of new units • Continuously monitoring and evaluating the operating costs • Setting attractive remuneration packages for the dormitory management
3	Limited possibility of using own funds Impact – medium Likelihood – small	WP1	• Ensuring sufficient resources for the project in the OU's reserve fund • Allocating only available funding from the OU's own resources • Communication with the OU faculties about the project state to coordinate the internal distribution of financial resources (university budget), ensure the financing of the project and allow a quick response to external changes
4	Extension of construction and delay in the project completion Impact – high Likelihood – high	WP2	• Envisaging a sufficient time reserve for the duration of the expected construction • Ensuring high-quality technical supervision of the contractor by the investor • Setting binding construction milestones with sanctions for non-compliance
5	Extension of procurement procedures and increase of procurement costs Impact – high Likelihood – high	WP2	• Developing high-quality project documentation • Ensuring efficient project team management • Managing responsibly the procurement planning by ensuring maximal consistency and accuracy in the procurement process • Implementation of solid procurement risk management practices to mitigate unforeseen complications in the process

DESCRIPTION OF THE ACTION (PART B)

COVER PAGE

PROJECT	
Project number:	101192431
Project name:	Affordable student housing for the University of Ostrava
Project acronym:	2024-6-CZ-Dormitory
Call:	JTM-2022-2025-PSLF
Topic:	JTM-2022-2025-PSLF-STANDALONE-PROJECTS
Type of action:	JTM-LS
Service:	CINEA/B/02
Project starting date:	12/06/2025
Project duration:	24 months

TABLE OF CONTENTS

1	RELEVANCE AND IMPACT	2
1.1	Background and general objectives	2
1.2	Needs analysis and specific objectives	2
1.3	Complementarity with other actions and innovation	3
1.4	Impact and ambition	3
2	QUALITY	5
2.1	Concept and methodology	5
2.2	Readiness and technical maturity.....	5
2.3	Financial maturity	6
2.4	Project management, quality assurance and monitoring and evaluation strategy	6
2.5	Cost effectiveness and financial management	8
2.6	Communication, dissemination and visibility.....	8
2.7	Sustainability and continuation.....	8
3	TIMETABLE.....	9

1 RELEVANCE AND IMPACT

1.1 Background and general objectives

The University of Ostrava is one of the main public institutions in Czechia's higher education system. It is located in Ostrava, one of the social, economic, and educational centres of Czechia. It is the third largest city in the country and the largest city in the Moravian-Silesian Region, a so-called structurally affected region. The development dynamics of the entire region are largely dependent on the development dynamics of the City of Ostrava.

The economy and employment of the City of Ostrava, its economic potential and current structure are strongly influenced by previous long-term historical developments. Economic development in the last two decades can be evaluated relatively positively. However, the demographic development is characterized by negative tendencies. Population decline is due to natural and socio-economic factors. Therefore, the construction of student dormitories will serve not only the needs of the university but the current and future needs of the labour market.

The University of Ostrava, as one of the two public universities in Ostrava, has a significant role in the correction of the structural affliction of the region as well as in its transformation into a modern post-industrial region not dependent on one dominant economic segment. Since its foundation in 1991, the University of Ostrava has created numerous educational opportunities in humanities, social sciences, arts, and natural sciences in a strongly industrialised region (also in terms of education). Subsequently, the university expanded the range of education to healthcare and medical fields. Today, it has over 160 study programmes in various fields. Such a broad offer is particularly important for the region, especially regarding preventing the outflow of existing residents and attracting new ones. Part of the strategic plans of both the Moravian-Silesian Region and the city of Ostrava is not only to maintain existing residents in the region by providing a wide range of educational opportunities, but also to attract new students from other regions and abroad with the aim of keeping these students in the region.

The university is an integral part of the Statutory City of Ostrava and the Moravian-Silesian Region. From 2017 to 2023, it was involved in the implementation of the objectives set out in the "Strategy of Economic Restructuring of Usti, Moravian-Silesian and Karlovy Vary Regions" which is based on Government Resolution No. 3 (January 9, 2017).

The University of Ostrava and its partners have a high professional potential with the ambition to become a centre of excellence in selected medical, natural science, biomedical and behavioural fields, and create a common basis for education and a scientific-research pillar supporting the transformation of the region.

However, further development, among other things, encounters barriers associated with insufficient infrastructural background outside of the professional career. The possibility of expanding the team to include potential students of new study programmes, highly skilled national and foreign workers who will play a key role in the education of future scientists continuing in R&D activities at the OU and in the region, is also conditional on building housing being available for students and junior scientists. In this respect, the creation of new accommodation fits into the overall concept of restructuring the region and is an integral part of the infrastructure that implements the change itself.

Territorial Just Transition Plan

Operational Programme Just Transition (OPJT) 2021-2027 / 26th September 2022

1.2 Needs analysis and specific objectives

Latest student enrolment data shows that the number of students has risen for the fifth consecutive year as well as demand for accommodation. In the academic year 2022-2023, the number of students enrolled at the Ostrava University approached 10,000. In recent years, the University of Ostrava has also seen a steady increase of foreign students from 887 foreign students, representing 10.5 % of the total number of students in the academic year 2018-2019, to 1121 foreign student, representing 12.4 % of the total number of students in the academic year 2022-2023.

The University of Ostrava places great emphasis on internationalisation in its strategic plan. In the future, it expects an even higher increase in foreign students, which is mainly related to the development of study programmes in a foreign language and the NEOLAiA (European University Alliance) project. One of the foreign language study programmes, for which it is also necessary to ensure accommodation, is the newly accredited General Medicine in English. The number of applicants who apply to the OU from regions other than Moravia-Silesia is also increasing.

The existing accommodation is insufficient not only in terms of capacity but especially in terms of contemporary requirements for modern accommodation facilities. In order for the University of Ostrava to be able to continue

helping the region with the growing problem of population outflow, it is necessary to increase its accommodation capacity.

1.3 Complementarity with other actions and innovation

This project is linked to other projects implemented by the University which have transformed part of the city centre into the Campus of the University of Ostrava (<https://citycampus.osu.cz/>) where new trainers, professors, production workers, graphic artists and musicians receive education. These projects also concern the creation of new/modification of the existing study programmes by strengthening practical teaching, involving future employers in the accreditation process, cooperating with other universities in the region in order to support the development needs of Moravia-Silesia.

Newly accredited study programmes prepare graduates who will address the specific needs of the region within the framework of the Strategic Framework for Economic Restructuring, especially in the rapidly developing segments of the IT and biotech market. At the same time, a background for the scientific project HAIE – Healthy Aging in Industrial Environment (<https://www.4haie.cz/haie/>), focusing on issues related to life in areas affected by industry, there has been created.

In the framework of the Just Transition Operational Programme, the University has also implemented its strategic project – LERCO (www.lerco.cz) – as well as the largest transformational project – REFRESH (<https://www.smaragdova.cz/refresh>).

The Life Environment Research Centre Ostrava (LERCO) is a newly built scientific research hub which is one of the tools enabling the transformation of the Moravian-Silesian Region from a "coal" to a "healthier and smarter" region. The project's 9 excellent research teams will conduct research activities with a broad and unique interdisciplinary focus on the biomedical, natural, and behavioural fields. The project is aimed at improving the quality of life of the population of the region.

The REFRESH project will build a unique European infrastructure for research and technology transfer in the fields of sustainable energy, digitalisation of industrial production, automation in transport, environmental technologies or smart material technologies with a socio-economic impact. The project will contribute to the transformation of the region towards a smart and green region. The main objective of the REFRESH project is to create a robust innovation ecosystem in the Moravian-Silesian Region in four areas: new energy; automation and robotics in manufacturing and transport; digitalisation; novel materials and environmental technologies, including their socio-economic dimension.

The project has a European dimension, as the University of Ostrava is involved in the Erasmus programme and has more than 400 student exchange agreements with partner universities across the European Union. Ensuring sufficient accommodation capacity for Erasmus exchange students is a very important aspect of the OU's further development. Given the existing housing capacity, there is limited accommodation for Erasmus students. A wider accommodation offer will allow the OU to further develop this cooperation and offer the possibility of an exchange stay to a larger number of students. In a similar way, the University of Ostrava is limited in the implementation of Joint Degree and Multiple Degree study programmes. As a result, all EU Member States will benefit indirectly from the expanded accommodation capacity of the OU.

The project is complementary to the activities included in the Territorial Just Transition Plan. The construction of the new dormitory will meet the requirements for environmentally friendly solutions and the reduction of greenhouse gas production using solar energy, energy from heat pumps connected to underground wells, greywater recycling, etc. Furthermore, the project addresses the development needs of a structurally affected region by supporting infrastructure for education and research.

1.4 Impact and ambition

Impact and ambition

The construction of new accommodation facilities of the University of Ostrava is important for the development of the region, as it will contribute to the further transformation of its social and economic structure which has been strongly influenced by its industrial past. The Moravian-Silesian region is still struggling with the population outflow, and it is therefore important to work on measures that will, on the contrary, contribute to the arrival of new residents. The University of Ostrava, which is already attracting students and employees from other regions, also aims to contribute to this goal. Surveys among graduates of the University of Ostrava show that most of them remain in the region in which they graduated even five years after graduation. The University of Ostrava therefore plays an important role in attracting new residents, not only from other regions but also from abroad. In addition to an

attractive study offer, a necessary condition for achieving this goal is high-quality accommodation facilities with sufficient capacity.

The indicators which will be used to measure the project's achievement in line with the specific objectives include:

- Increase in the number of accommodation places in university dormitories of the University of Ostrava by 332 places
- Increase in the number of places for students with special needs (students with reduced mobility) - 4 rooms designed for 8 people (out of the total number of 332 places)
- Creation of 6 rooms suitable for parents with children (the university does not yet have this type of rooms)
- New jobs created – Total number = 7 (FTE), Male 2, Female 5 (newly created job positions ensuring the operation of student dormitory)
 - maintenance worker (1 FTE)
 - cleaners (4 FTE)
 - dormitory operations officer (1 FTE)
 - administrative position / International Student Officer (1 FTE)
- Persons reached / direct beneficiaries of the project (students living in dormitory and tourists staying in dormitory) - 4980 persons within a timeframe of 17 years, which corresponds to the estimated economic life of the project

The project addresses the following just transition challenges of the Moravian-Silesian Region:

- Mismatch in the labour market. Attracting new residents will contribute to higher availability of qualified labour for the segment of knowledge-intensive services. The profile of graduates of the University of Ostrava corresponds to the most demanded and dynamic industries in the city/region. It can also have a direct impact on the diversification of the city/regional economy.
- Business development. New residents can implement business plans that can develop the innovation ecosystem, thanks to the internal capacities of the University of Ostrava and tight cooperation with the Moravian-Silesian Innovation Centre.
- A small share of knowledge-intensive business services in the region's economy. As already mentioned, this segment shows a high degree of conformity with the profile of graduates from the University of Ostrava. Simultaneously, it is a key segment for the regional competitiveness.
- Declining population (highly uneven within the region) caused by emigration, compounded in the near future by the growing importance of natural demographic change (ageing).
- Despite their intensive progress, regional universities are still considered mid-range universities. The construction of student dormitories will make it possible to attract students from abroad, thereby increasing the internationalisation of the University of Ostrava which is a key prerequisite for increasing the university's status in the international context.
- The region still has not coped with its negative image which can have a negative effect not only on potential investors but also on the highly qualified workforce that is needed in the region. The project can contribute to improving the image of the city as a university city.
- Unsustainable development of the territory. Agricultural land encroachment continues to increase, and spatially dispersed development dominates. The project makes intelligent use of the existing built-up area, thereby increasing the density or environmental sustainability of the urban landscape.

Environmental impact

The new dormitory is expected to have lower energy and water consumption compared to the existing blocks. This will be achieved by using modern, ecological and energy-saving solutions, e.g. LED lights; ground source heat pumps (including recharging of ground source heat pump boreholes during the summer for cooling); photovoltaic panels on the roof; energy-efficient water taps; high-efficiency hot water heating using heat pumps; reducing the heat load by using shading elements on heat-stressed facades, use of high-quality thermal insulation; rainwater reuse, etc. The project envisages energy management based on metering the energy consumption so that these users can act in an environmentally conscious manner. Based on data obtained from designers, the estimated energy consumption per bed should be reduced from 2.45 to 1.5 kWh bed/year. Water consumption should be reduced from 18.12 litres/bed to 13.5 litres/bed. It is expected that the newly built accommodation capacity will be innovative in terms of energy management and serve as a model for building similar student accommodation projects.

The construction is not expected to have a negative environmental impact. It is planned on the site of the existing connecting tract, paved areas, and parking lot (existing drainage to the sewer). The existing building connection is in a very unsatisfactory condition, partially unusable and energy consuming. The new construction is planned largely on existing built-up areas, with stormwater being reused or soaked back into the bedrock. There is no massive cutting of greenery, and the cut greenery is replaced by new planting. Thanks to the use of modern and environmentally friendly technologies, no increase in emissions compared to the current situation is expected. The construction waste will be recycled and reused for backfilling sewers, retaining walls, etc.

Gender equality, non-discrimination and accessibility

The project will be gender-neutral as accommodation will be provided regardless of gender, race, religion, nationality or ethnic origin.

The accommodation will be available for parents with children. 6 rooms suitable for accommodation of families (students) with children will be built.

The project also envisages the placement of gender-neutral toilets in common areas.

Students will be able to choose their roommates. The accommodation will be provided on the "first come, first serve" principle, except for students with reduced mobility who will receive the priority for accommodation. In addition to the fact that all social spaces are designed to be accessible, it is planned to build four special rooms intended for students with special needs.

The project contains enough social spaces intended for individual and collective education and for spending leisure time. The possibility of preparing food is provided not only in each room with a small kitchenette, but also on each floor with a common kitchen with a dining room.

The use of drugs and smoking is prohibited in the entire campus of the student dormitories.

The university's gender policy is presented within the "Action Plan of Gender Equality at the University of Ostrava 2022-2025" (link: <https://dokumenty.osu.cz/osu/acction-plan-of-gender-equality-at-the-university-of-ostrava.pdf>). The University of Ostrava emphasizes the area of social security ("Practical Guide to Social Safety at the University of Ostrava" – link: <https://dokumenty.osu.cz/osu/pruvodci/prakticky-pruvodce-socialnim-bezpecim-en.pdf>), and regulates the rules for secure communication through an electronic system (Rector's Measure No. 22/2023). There was established a function of ombudsman to ensure a system of equal treatment.

2 QUALITY

2.1 Concept and methodology

Concept and methodology

The construction of a new dormitory owned directly by the University of Ostrava is the most suitable solution for the following reasons:

- The university will directly control the possibility of providing accommodation for students coming from other regions, and especially students of mobility programmes.
- The university will become more flexible in terms of accommodation and will not have to rely on commercial accommodation for students.
- The university will be able to provide affordable social housing, especially for foreign students from developing countries or students belonging to socio-economically disadvantaged groups.
- The university will acquire modern accommodation facilities corresponding to modern trends (including environmental ones).
- The new dormitory will have low energy consumption by using highly efficient ground borehole systems with heat pumps and photovoltaic panels on the roofs of the new buildings.
- The development of affordable and sustainable student housing will increase urban density and reduce the operating costs of the city.

The project is fully supported by local actors led by the Statutory City of Ostrava and its district where the building will be built, the Moravian-Silesian Region, as well as national actors under the leadership of the Ministry of Education, Youth and Sports.

The selection of the construction contractor will be carried out in full accordance with the national legislation on Public Procurement, and the relevant internal regulations of the University of Ostrava. The necessary technical qualification of the procurement procedure will be established to guarantee the selection of a contractor.

In the case of public procurement for the interior works, samples of the materials specified by the designers for the main elements of the interior will be part of the assessment to ensure a sufficiently high-quality and durable solution.

2.2 Readiness and technical maturity

The construction of the new accommodation capacity will be carried out on land owned by the University of Ostrava. The University of Ostrava already has a valid building permit for its construction.

As part of the implementation of the project, four procurement procedures are expected – for the construction contractor, for the construction manager, for the supplier of interior equipment, and the supplier of IT equipment. The implementation of procurement procedures will be entirely under the direction of the University of Ostrava which has sufficient professional and administrative capacity for this purpose.

2.3 Financial maturity

The total estimated costs for the construction and equipment of the new dormitory are CZK 453,597,241.00 without VAT (EUR 18,622,105.29). The project is financed with a loan from the National Development Bank totalling to CZK 127,000,000.00 (EUR 5,213,892.77), complemented by the PSLF grant, which represents 25 % of the loan, i.e. CZK 31,750,000.00 (EUR 1,303,473.19), as the project is in a less developed region. The remaining part of the investment costs will be covered by a subsidy from the Ministry of Education, Youth and Sports within a programme for the development and renewal of public higher education institutions, as well as regional subsidies (Moravian-Silesian Region and Statutory City of Ostrava).

Budget breakdown	CZK	EUR *
Total costs	453,597,241.00	18,622,105.29
EIB/NRB Loan	127,000,000.00	5,213,892.77
EU Grant	31,750,000.00	1,303,473.19
Own resources	294,847,241.00	12,104,739.33


* Exchange rate: EUR 1 = CZK 24.358 (European Central Bank rate as of 13/10/2025, the day of loan signing).

2.4 Project management, quality assurance and monitoring and evaluation strategy

Project management is an integral part of the processes taking place within individual centres and departments of the university. At the rectorate level, the Centre for Development and Strategy with its Project Support Unit is both the main methodological centre for project activities and the project management point for strategic projects of the university. The advantage of this setting can be seen in cases where the methodological part of the department is ready to set the rules for project management directly in the context of the course of individual projects. Possible risks arising within the project activities are dealt with and the method of solution is automatically transferred to other ongoing or upcoming projects. Project management itself is thus not limited by the specialisation of individual managers and, thanks to the diversification of project activities (research, development, investment, national, international, etc.), enables a multi-criterion view of possible risks, their prevention and the solution of their consequences.

The organisational structure of the projects is set at three levels, in descending order according to the degree of authority and responsibility:

1. Project management level (project guarantor / university management representatives)
2. Operational level of the project (project management team)
3. Implementation level (project teams)

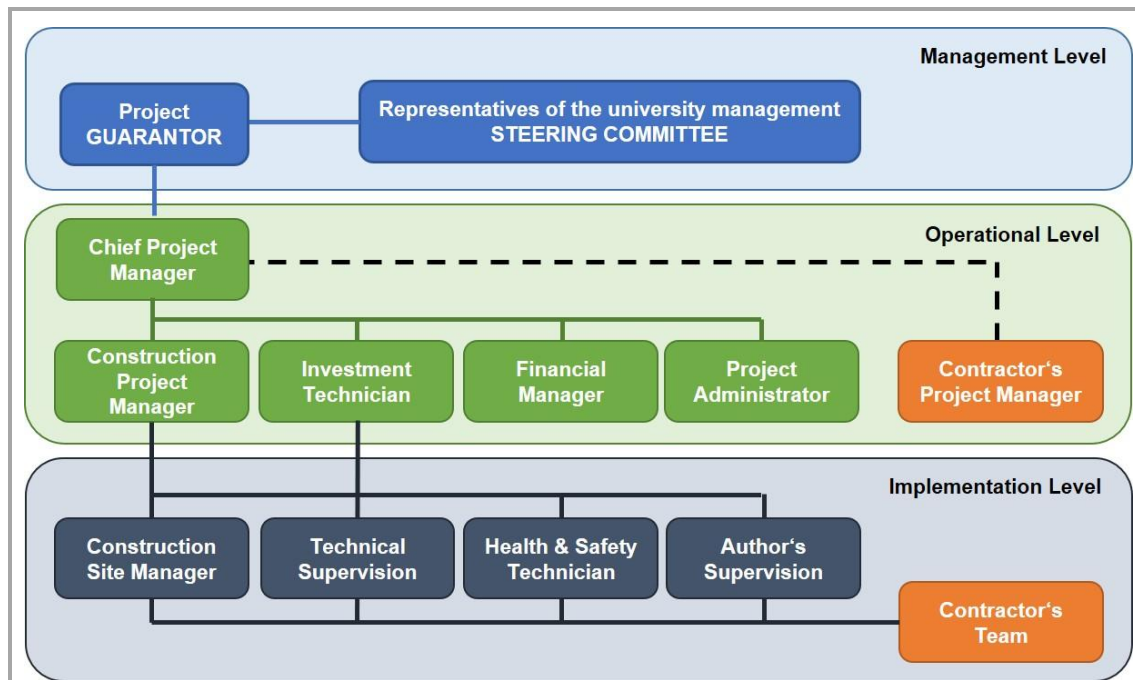

Project management structure

The main support system for project management is MS Teams. The project is managed in MS Project where important milestones that will be monitored and continuously evaluated are set. Delays in the completion of selected milestones as well as in the completion of the entire construction will be subject to sanctions against the construction contractor. After the start of the construction, regular inspection days will be set up with the Construction Contractor, Lead Designer, Construction Manager, Project Manager and Financial Manager. Based on the long-term practice of the University of Ostrava during construction, the weekly regime of these control days has proven to be effective.

The important indicators that will be monitored are the progress and quality of the construction works. The construction site manager will be responsible for monitoring the indicators in cooperation with the lead designer, who also fulfills the role of author supervision. The indicators will be evaluated on a weekly basis.

Another important indicator is the financial consumption of the budget and the correct accounting of individual budget items. The financial manager of the project will be responsible of the budget consumption together with the construction manager who will provide the documents for invoicing (the so-called list of completed works).

During construction, there may be a need to create change order sheets for more or less work. At the implementation level, the construction manager will be responsible for monitoring and evaluating the need to conclude the change order sheets and subsequently the amendment to the contract in cooperation with the lead designer.

Similar to the setting of the organisational structure, it is important to ensure operational responses to any problems and risks to avoid that the project objectives are jeopardised. The following rules for problem escalation are established within the project:

- Current problems/risks that arise during project implementation are primarily resolved at the level at which they arise, in accordance with defined responsibilities and powers for individual project roles.
- Any member of the project team can draw attention to a problem that occurs during the implementation of the project verbally or in a formal way (via e-mail, or the MS Teams IT tool), and always to their direct superior in the project structure who is obliged to solve the problem or raise it to a higher project level.
- The person who is responsible for solving the problem/risk, according to the content of their work role, prepares a proposal for a solution, including deadlines and responsibilities. The approved solution is subsequently called up. The person responsible for the solution evaluates and informs the assigner of the task. If necessary, the assigner of the task informs the Management Level about the method of resolution.
- To resolve any disagreements and problems that may arise during the implementation of the project, escalation from the bottom up along individual lines of the organizational structure will be used (implementation level → operational level → management level).

The broader project team will also include a lawyer employed by the legal department of the University of Ostrava, who will supervise the contractual documentation associated with the project.

The project manager will include the schedule of individual public contracts in the Project Schedule, defining the time for the preparation of the public procurement and considering the time of its submission, the time required for

the evaluation of bids and the selection of the winning bidder, as well as the time required for securing the signature of the contract.

The Department of Public Procurement of the University of Ostrava will be responsible for the announcement of the procurement procedure and its implementation and will prepare the procurement documentation in cooperation with the Chief Project Manager, the investment technician, and the legal department. The planned procurement procedures are included in the University's public procurement plan.

2.5 Cost effectiveness and financial management

The financial management of projects implemented by the OU is primarily governed by the current internal regulations covering financial management, budget, and internal control system.

For co-financed projects, the financial management of the project is additionally governed by the provisions of the relevant provider of financing. In the event of a conflict, the priority is given to the provider's rules.

The Financial Manager (Budget Manager) is responsible for the financial management of the project to the extent determined by the role description. If this role is not specified in the project, the Project Manager, who also acts as Deputy Budget Manager, carries the responsibility for financial management. To perform his role, the Budget Manager cooperates, when necessary, with the Operation Assignment Manager, who is the Project Guarantor, and the deputy is the Chief Project Manager.

The project will comply with the 3E principle, i.e., procurement will be carried out in line the effectiveness, efficiency and economics criteria. Checks for compliance with the applicable conflict of interest rules and sanction lists will also be performed.

In the implementation phase, the university will monitor whether the delivered values meet the 3E criteria and whether there is a risk of violation of these criteria. the selected Construction Site Manager will control the entire construction process, monitor whether the construction is in accordance with the quality standards set in the project documentation for the construction, and manage other construction-related activities (mainly technical supervision of the investor, health and safety control, budget control, supervision of change order sheets).

A subsequent check carried out by the internal auditor will evaluate whether the 3E procurement criteria defined at the beginning have been followed. The internal evaluation is then used as a basis for the preparation of new internal regulations for project solutions.

2.6 Communication, dissemination and visibility

The communication activities will target primarily students from other regions and countries, Erasmus+ students, project stakeholders, non-study persona assistants or student guides, guests of the University, and other candidates for OU's housing as well as the citizens of Ostrava.

In accordance with the applicable communication rules for the EU-funded projects, the EU flag and co-funding statement will be displayed to give visibility to the EU support in all communication materials.

2.7 Sustainability and continuation

The maintenance and operation of the project will be completely under the responsibility of the University of Ostrava. The maintenance and operation costs will be covered with rental revenues and financial contribution of the university.

Project: 101192431 — 2024-6-CZ-Dormitory — JTM-2022-2025-PSLF

3 TIMETABLE

WP no.	WP	Task no.	Task	GA planning					2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
									Q1			Q2			Q3			Q4			Q1			Q2			Q3			Q4			Q1			Q2			Q3			Q4																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
				Start date	End date	Start month	End month	Duration	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
1	Project management and communication			12/06/2025	31/05/2027	1	24							1	2	3	4	5	6	7																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																</

M – Milestone
D – Deliverable

Project: 101192431 — 2024-6-CZ-Dormitory — JTM-2022-2025-PSLF

HISTORY OF CHANGES		
VERSION	PUBLICATION DATE	CHANGE
1.0	01.06.2022	Initial version (new MFF).

ANNEX 2

ESTIMATED BUDGET (LUMP SUM BREAKDOWN) FOR THE ACTION

Forms of funding	Estimated EU contribution		
	Estimated eligible lump sum contributions (per work package)		Maximum grant amount ¹
	WP1 Project management and communication	WP2 Construction of the new dormitory	
	Lump sum contribution	Lump sum contribution	
	a	b	c = a + b
1 - OU	0.00	1 303 473.19	1 303 473.19

¹ The 'maximum grant amount' is the maximum grant amount fixed in the grant agreement (on the basis of the sum of the beneficiaries' lump sum shares for the work packages).

ANNEX 4 XXX LUMP SUM MGA — MULTI & MONO

FINANCIAL STATEMENT FOR THE ACTION FOR REPORTING PERIOD [NUMBER]

EU contribution												
Eligible lump sum contributions (per work package)												Requested EU contribution
	WP1 [name]	WP2 [name]	WP3 [name]	WP4 [name]	WP5 [name]	WP6 [name]	WP7 [name]	WP8 [name]	WP9 [name]	WP10 [name]	WP [XX]	
Forms of funding	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	[Lump sum contribution// Financing not linked to costs]	
Status of completion	COMPLETED	COMPLETED	COMPLETED	COMPLETED	COMPLETED	COMPLETED	COMPLETED	PARTIALLY COMPLETED	PARTIALLY COMPLETED	COMPLETED	NOT COMPLETED	
	a	b	c	d	e	f	g	h	i	j	k	$l = a + b + c + d + e + f + g + h + i + j + k$
1 – [short name beneficiary]												
1.1 – [short name affiliated entity]												
2 – [short name beneficiary]												
2.1 – [short name affiliated entity]												
X – [short name associated partner]												
Total consortium												

The consortium hereby confirms that:

The information provided is complete, reliable and true.

The lump sum contributions declared are eligible (in particular, the work packages have been completed and the work has been properly implemented and/or the results were achieved; see Article 6).

The proper implementation of the action/achievement of the results can be substantiated by adequate records and supporting documentation that will be produced upon request or in the context of checks, reviews, audits and investigations (see Articles 19, 21 and 25).

ANNEX 5

SPECIFIC RULES

INTELLECTUAL PROPERTY RIGHTS (IPR) — BACKGROUND AND RESULTS — ACCESS RIGHTS AND RIGHTS OF USE (— ARTICLE 16)

Rights of use of the granting authority on results for information, communication, dissemination and publicity purposes

The granting authority also has the right to exploit non-sensitive results of the action for information, communication, dissemination and publicity purposes, using any of the following modes:

- **use for its own purposes** (in particular, making them available to persons working for the granting authority or any other EU service (including institutions, bodies, offices, agencies, etc.) or EU Member State institution or body; copying or reproducing them in whole or in part, in unlimited numbers; and communication through press information services)
- **distribution to the public** in hard copies, in electronic or digital format, on the internet including social networks, as a downloadable or non-downloadable file
- **editing** or **redrafting** (including shortening, summarising, changing, correcting, cutting, inserting elements (e.g. meta-data, legends or other graphic, visual, audio or text elements) extracting parts (e.g. audio or video files), dividing into parts or use in a compilation
- **translation**(including inserting subtitles/dubbing)in all official languages of EU
- **storage** in paper, electronic or other form
- **archiving** in line with applicable document-management rules
- the right to authorise **third parties** to act on its behalf or sub-license to third parties, including if there is licensed background, any of the rights or modes of exploitation set out in this provision
- **processing**, analysing, aggregating the results and **producing derivative works**
- **disseminating** the results in widely accessible databases or indexes (such as through ‘open access’ or ‘open data’ portals or similar repositories), whether free of charge or not.

The beneficiaries must ensure these rights of use for the whole duration they are protected by industrial or intellectual property rights.

If results are subject to moral rights or third party rights (including intellectual property rights or rights of natural persons on their image and voice), the beneficiaries must ensure that they

comply with their obligations under this Agreement (in particular, by obtaining the necessary licences and authorisations from the rights holders concerned).

COMMUNICATION, DISSEMINATION AND VISIBILITY (— ARTICLE 17)

Communication and dissemination plan

The beneficiaries must provide a detailed communication and dissemination plan, setting out the objectives, key messaging, target audiences, communication channels, social media plan, planned budget and relevant indicators for monitoring and evaluation.

Additional communication and dissemination activities

The beneficiaries must engage in the following additional communication and dissemination activities:

- **present the project** (including project summary, coordinator contact details, list of participants, European flag and funding statement and project results) on the beneficiaries' **websites** or **social media accounts**
- for actions involving equipment, infrastructure or works, display public **plaques** or **billboards** as soon as the work on the action starts and a **permanent commemorative plaque** once it is finished, with the European flag and funding statement
- upload the public **project results** to the JTM Project Results platform, available through the Funding & Tenders Portal.

SPECIFIC RULES FOR CARRYING OUT THE ACTION (— ARTICLE 18)

Durability


Unless exempted by the granting authority, the beneficiaries must commit to continue to use and maintain after the end of the action equipment funded under this grant agreement, for activities pursuing the action's objectives. Such equipment must be used for these purposes — for at least five years after the end of the action (see Data Sheet, Point 1) or until the end of its economic lifespan (i.e. until it has been fully depreciated) — whichever is earlier.

Specific rules for blending operations

When implementing blending operations, the beneficiaries acknowledge and accept that:

- the grant depends on the approved financing from the Implementing Partner
- the amount of the grant depends on the amount of the loan granted by the Implementing Partner (and will be reduced if the final amount of the loan is reduced)
- they must inform the granting authority both about the approval for financing, the entry into force of the financing agreement and the financial close — within 15 days
- the payment deadline for the first prefinancing is automatically suspended until the granting authority is informed about the financial close
- both actions will be managed and monitored in parallel and in close coordination with the Implementing Partner, in particular:

- all information, data and documents (including the due diligence by the Implementing Partner and the signed agreement) may be exchanged and may be relied on for the management of the other action (if needed)
- issues in one action may impact the other (e.g. suspension or termination in one action may lead to suspension also of the other action; termination of the grant will normally suspend and exit from further financing and vice versa, etc.)
- the granting authority may disclose confidential information also to the Implementing Partner.

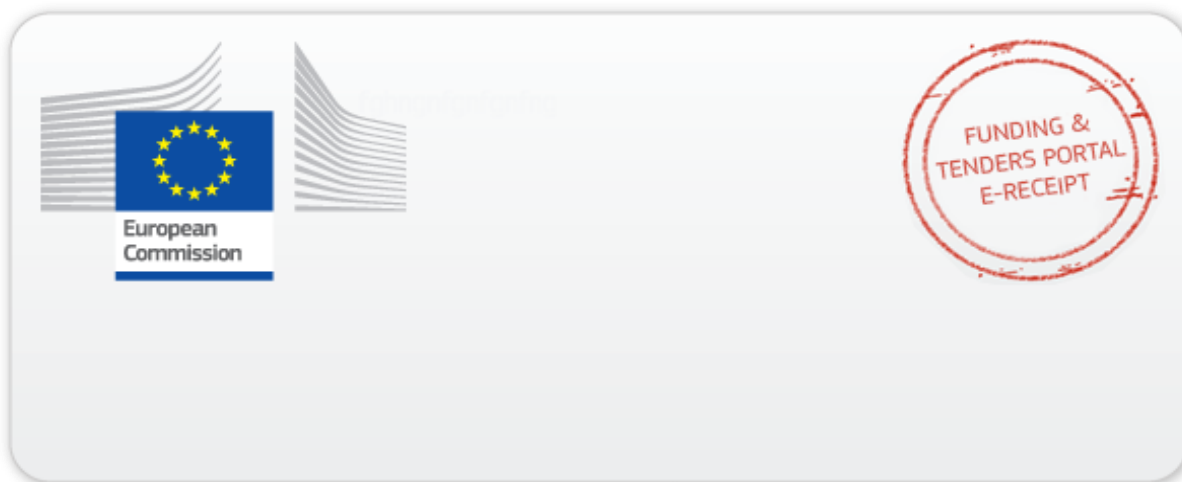

This electronic receipt is a digitally signed version of the document submitted by your organisation. Both the content of the document and a set of metadata have been digitally sealed.

This digital signature mechanism, using a public-private key pair mechanism, uniquely binds this eReceipt to the modules of the Funding & Tenders Portal of the European Commission, to the transaction for which it was generated and ensures its full integrity. Therefore a complete digitally signed trail of the transaction is available both for your organisation and for the issuer of the eReceipt.

Any attempt to modify the content will lead to a break of the integrity of the electronic signature, which can be verified at any time by clicking on the eReceipt validation symbol.

More info about eReceipts can be found in the FAQ page of the Funding & Tenders Portal.

(<https://ec.europa.eu/info/funding-tenders/opportunities/portal/screen/support/faq>)
